ಕಂಡಿಕೆ ಸಂಖ್ಯೆ	ಟಿಪ್ಪಣಿಗಳು ಮತ್ತು ಆಜ್ಞೆಗಳು

ಮಂಡಿಸಿದೆ.

ವಿಷಯ: Resurfacing of roads at Maruthinagara 3rd main 6th, 7th and 8th cross roads in kempegowda ward no -01.

* * * * *

ಮೇಲ್ಕಂಡ ವಿಷಯಕ್ಕೆ ಸಂಬಂದಿಸಿದಂತೆ, ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ ಯಲಹಂಕ ಉಪ ವಿಭಾಗದ ಕೆಂಪೇಗೌಡ ವಾರ್ಡ್ ನಂ–01ರ ವ್ಯಾಪ್ತಿಯಲ್ಲಿನ ಮಾರುತಿನಗರದ 3ನೇ ಮುಖ್ಯರಸ್ತೆ ಮತ್ತು ಅಡ್ಡರಸ್ತೆಗಳಲ್ಲಿ ಚರಂಡಿ ಮತ್ತು ರಸ್ತೆ ಅಭಿವೃದ್ದಿಪಡಿಸಿಕೊಡಬೇಕೆಂದು ಸ್ಥಳೀಯ ಸಾರ್ವಜನಿಕರು ಯಲಹಂಕ ವಿಧಾನ ಸಭಾ ಕ್ಷೇತ್ರದ ಮಾನ್ಯ ಶಾಸಕರಿಗೆ ಮನವಿಯನ್ನು ಸಲ್ಲಿಸಿರುತ್ತಾರೆ. ಮುಂದುವರೆದು ಯಲಹಂಕ ವಿಧಾನ ಸಭಾ ಕ್ಷೇತ್ರದ ಮಾನ್ಯ ಶಾಸಕರು ಸದರಿ ಕಾಮಗಾರಿಯನ್ನು ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆಯ 2024–25ನೇ ಸಾಲಿನ ಆಯವ್ಯಯದ ಲೆಕ್ಕ ಶಿರ್ಷಿಕೆ 05–330502ಅಡಿಯಲ್ಲಿ ಹಿಂದುಳಿದ ವರ್ಗದವರ ಕಲ್ಯಾಣ ನಿಧಿ ಕಾಮಗಾರಿಗಳು / ಮೂಲಭೂತ ಸೌಕಾರ್ಯ ಅಭಿವೃದ್ದಿ ಕಾಮಗಾರಿಗಳಿಗೆ ಮೀಸಲಿಟ್ಟಿರುವ ಅನುದಾನದಡಿಯ ಸೇರಿ ಆರ್.ಸಿ.ಸಿ. ಚರಂಡಿ ನಿರ್ಮಾಣ ಮಾಡಿ ಸದರಿ ಪ್ರದೇಶಗಳನ್ನು ಅಭಿವೃದ್ದಿಪಡಿಸುವಂತೆ ತಿಳಿಸಿರುತ್ತಾರೆ.

ಅದರಂತೆ ಸ್ಥಳ ಪರಿವೀಕ್ಷಣೆ ಮಾಡಿ ಈ ಮೇಲ್ಕಂಡ ಕಾಮಗಾರಿಯನ್ನು 2024–25ನೇ ಸಾಲಿನ ಆಯವ್ಯಯದ ಅನುದಾನದಡಿಯಲ್ಲಿ ಸೇರಿಸಿ ಲೆಕ್ಕಶಿರ್ಷಿಕೆ 05–330502ರ ಕಾರ್ಯಕ್ರಮದಡಿಯಲ್ಲಿ **ರೂ.೫೦.೦೦ಲಕ್ಷಗಳಿಗೆ** ಅಂದಾಜು ಪಟ್ಟಿಯನ್ನು ಲೋಕೋಪಯೋಗಿ ಇಲಾಖೆ 2023–24ನೇ ಸಾಲಿನಲ್ಲಿ ಮಂಜೂರಾಗಿರುವ ದರಪಟ್ಟಿಯಂತೆ ತಯಾರಿಸಲಾಗಿದೆ.ಸದರಿ ಅಂದಾಜು ಪಟ್ಟಿಯಲ್ಲಿ ಈ ಕೆಳಕಂಡ ಅಂಶಗಳು ಒಳಗೊಂಡಿರುತ್ತದೆ.

1. ಆರ್.ಸಿ.ಸಿ ಚರಂಡಿ ನಿರ್ಮಾಣ ಮಾಡಲು ಮಣ್ಣು ಅಗೆತ ಕೆಲಸ ಮಾಡುವುದು.
2. ತೆಗೆದ ಮಣ್ಣನ್ನು ದೂರದ ಸ್ಥಳಕ್ಕೆ ಸಾಗಿಸುವುದು.
3. ಆರ್.ಸಿ.ಸಿ ಚರಂಡಿಯ ತಳಪಾಯಕ್ಕೆ 1:4:8 ಮೀಶ್ರಣದ ಕಾಂಕ್ರೀಟ್ ಹಾಕುವುದು.
4. ಆರ್,ಸಿ,ಸಿ ಚರಂಡಿಗೆ ಉಕ್ಕಿನ ಸರಳುಗಳನ್ನು ಅಳವಡಿಸುವುದು.
5. ಆರ್.ಸಿ.ಸಿ ಚರಂಡಿಗೆ ಎಂ–20 ಮೀಶ್ರಣದ ಕಾಂಕ್ರೀಟ್ ಹಾಕಿ ಚರಂಡಿಯ ಮೇಲೆ ಆರ್.ಸಿ.ಸಿ ಪ್ರಿ ಕ್ಯಾಸ್ಟ್ ಕವರಿಂಗ್ ಕಲ್ಲುಗಳನ್ನು ಅಳವಡಿಸುವುದು.
6. ರಸ್ತೆಗಳಿಗೆ ವೆಟ್ ಮಿಕ್ಸ್ ಹರಡುವುದು ಮತ್ತು ಪ್ರೈಮರ್ ಕೋಟ್ ಮತ್ತು ಟ್ಯಾಕ್ ಕೋಟ್ ಅಂಟು ಪದರ ಲೇಪಿಸುವುದು.
7. ರಸ್ತೆಗಳಿಗೆ ಬಿ.ಎಂ. ಮತ್ತು ಬಿ.ಸಿ. ಡಾಂಬರೀಕರಣ ಮಾಡುವುದು ಇತ್ಯಾಧಿ.

ಮೇಲ್ಕಂಡ ಎಲ್ಲಾ ಅಂಶಗಳು ಸದರಿ ಕಾಮಗಾರಿಗೆ ಬಹಳ ಅವಶ್ಯಕವಾಗಿರುತ್ತದೆ. ಅದ್ದರಿಂದ ಇವುಗಳನ್ನು ಅಳವಡಿಸಿ ಅಂದಾಜು ಪಟ್ಟಿಯನ್ನು ತಯಾರಿಸಲಾಗಿದೆ. ಈ ಕಾಮಗಾರಿಗೆ 2024–25ನೇ ಸಾಲಿನ ಆಯವ್ಯಯದ ಅನುದಾನದಡಿಯಲ್ಲಿ ಸೇರಿಸಿ ಲೆಕ್ಕಶಿರ್ಷಿಕೆ 05–330502 ರಡಿ ಜಾಬ್ ಸಂಕೇತ _____ರಂತೆ ಕಾಮಗಾರಿಯ ಸಂಕೇತ ದೊರೆತಿದ್ದು ಕೆಲಸವನ್ನು ತುರ್ತಾಗಿ ತೆಗೆದುಕೊಳ್ಳಬೇಕಾಗಿರುವುದರಿಂದ ಹಾಗೂ ಟೆಂಡರ್ ಪ್ರಕ್ರಿಯೆ ಕೈಗೊಳ್ಳಲು ಈ ಅಂದಾಜು ಪಟ್ಟಿಗೆ ಆಡಳಿತಾತ್ಮಕ ಹಾಗೂ ತಾಂತ್ರಿಕ ಮಂಜೂರಾತಿ ಕೋರಿ ಕಡತವನ್ನು ತಮ್ಮ ಮುಂದಿನ ಆದೇಶಕ್ಕೆ ಮಂಡಿಸಿದೆ.

Ramadevi

ಸ.ಕಾ.ಅ (ಯ.ಉ.ವಿ)

ಸಿಅ

ಕಂಡಿಕೆ ಸಂಖ್ಯೆ

ಟಿಪ್ಪಣಿಗಳು ಮತ್ತು ಆಜ್ಞೆಗಳು

6) EE (yelahanka)

ಕಂಡಿಕೆ (05) ರಲ್ಲಿ ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು, ಯಲಹಂಕ ಉಪವಿಭಾಗರವರು ಮಾಡಿರುವ ಪ್ರಸ್ತಾವನೆಯಂತೆ 2024–25ನೇ ಸಾಲಿನ ಆಯವ್ಯಯದ ಲೆಕ್ಕಶೀರ್ಷಿಕೆ 05–330502ರಡಿ ಹಿಂದುಳಿದ ವರ್ಗದವರ ಕಲ್ಯಾಣ ನಿಧಿ ಕಾಮಗಾರಿಗಳ ಮೂಲಭೂತ ಸೌಕರ್ಯ ಅಭಿವೃದ್ಧಿ ಯೋಜನೆಯಡಿಯಲ್ಲಿ ಮೀಸಲಿಟ್ಟಿರುವ ಅನುದಾನದಡಿಯಲ್ಲಿ ಮಂಜೂರಾಗಿರುವ "Resurfacing of roads at Maruthinagara 3rd main 6th, 7th and 8th cross roads in Kempegowda ward no -01" ಎಂಬ ಕಾಮಗಾರಿಯನ್ನು ಕೈಗೊಳ್ಳಲು 2023–24ನೇ ಸಾಲಿನ ಲೋಕೋಪಯೋಗಿ ಇಲಾಖೆಯ ಎಸ್.ಆರ್. ದರಪಟ್ಟಿ ಅನುಸರಿಸಿ ರೂ.50.00ಲಕ್ಷಗಳಿಗೆ ಅಂದಾಜುಪಟ್ಟಿಯನ್ನು ತಯಾರಿಸಲಾಗಿದ್ದು, ಸದರಿ ಅಂದಾಜು ಪಟ್ಟಿಗೆ ಮಾನ್ಯ ಮುಖ್ಯ ಆಯುಕ್ತರವರು ಅಧಿಕಾರ ಪ್ರತ್ಯಾಯೋಜಿಸಿ ಹೊರಡಿಸಿರುವ ಆದೇಶ ಸಂಖ್ಯೆ:ಬಿ12(1) ಪಿ.ಆರ್/394/2023–24 ದಿನಾಂಕ:06–12–2023ರಂತೆ ನೀಡಿರುವ ಅಧಿಕಾರದನ್ವಯ ಸದರಿ ಕಾಮಗಾರಿಗೆ ಆಡಳಿತಾತ್ಮಕ ಅನುಮೋದನೆ, ತಾಂತ್ರಿಕ ಮಂಜೂರಾತಿ ಹಾಗೂ ಡಿ.ಟಿ.ಎಸ್. ಅನುಮೋದನೆ ನೀಡಲು ತಮ್ಮ ಮುಂದಿನ ಆದೇಶ ಕೋರಿ ಸಲ್ಲಿಸಿದೆ.

07/05/2025

Executive Engineer
Bruhat Bangalore Mahanagara Palike
Yelahanka, Division

(7) ಮುಖ್ಯ ಅಭಿಯಂತರರು (ಯಲಹಂಕ ವಲಯ)

ಕಂಡಿಕೆ (1) ರಿಂದ (6)ರ ವರೆಗಿನ ವರದಿಯಂತೆ ಹಾಗೂ ಮಾನ್ಯ ಮುಖ್ಯ ಆಯುಕ್ತರ ಕಛೇರಿ ಆದೇಶ ಸಂಖ್ಯೆ:ಬಿ12(1)ಪಿಆರ್/394/2023–24, ದಿನಾಂಕ:06–12–2023ರಂತೆ ಮೇಲ್ಕಂಡ ಪ್ರಸ್ತಾವನೆಯ ಅಂದಾಜುಪಟ್ಟಿ ಮೊತ್ತ ರೂ50.00ಲಕ್ಷಗಳಿಗೆ ಆಡಳಿತಾತ್ಮಕ ಅನುಮೋದನೆ ಕೋರಿ ಕಡತವನ್ನು ಮಂಡಿಸಿದೆ.

ಮುಖ್ಯ ಅಭಿಯಂತರರು (ಯಲಹಂಕ ವಲಯ)
ಯಲಹಂಕ ವಲಯ
ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ

(8) ವಲಯ ಆಯುಕ್ತರು (ಯ.ವ) ಅನುಮೋದಿಸಿದೆ 7/3/25

(9) EE (yelahanka - Division)

ವಿಷಯ Re-Surfacing of roads in Maruthinagara 3rd main, 6

ಕಂಡಿಕೆ ಸಂಖ್ಯೆ

(10)

(11)

Nagara 3rd main 6th, 7th & 8th Cross roads in Ward No-01

ಕಂಡಿಕೆ ಸಂಖ್ಯೆ | ಕಡತದ ಸಂಖ್ಯೆ

ಟಿಪ್ಪಣಿಗಳು ಮತ್ತು ಆಜ್ಞೆಗಳು

(10) ಕಂಡಿಕೆ (05) ರಲ್ಲಿ ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು ಯಲಹಂಕ ಉಪವಿಭಾಗರವರು ಮಾಡಿರುವ ಪ್ರಸ್ತಾವನೆಯಂತೆ 2024–25ನೇ ಸಾಲಿನ ಆಯವ್ಯಯದ ಲೆಕ್ಕಶೀರ್ಷಿಕೆ :05–330502ಅಡಿ ಹಿಂದುಳಿದ ವರ್ಗಗಳ ಕಲ್ಯಾಣ ನಿಧಿ ಅನುದಾನದಡಿಯಲ್ಲಿ ಮಂಜೂರಾಗಿರುವ Resurfacing of roads at Maruthinagara 3rd main 6th, 7th and 8th cross roads in Kempegowda ward no -01ಎಂಬ ಕಾಮಗಾರಿಯನ್ನು ಕೈಗೊಳ್ಳಲು ಎಲೆಕ್ಟ್ರಿಕಲ್ ದರಪಟ್ಟಿಯನ್ನು ಅನುಸರಿಸಿ ರೂ.50.00ಲಕ್ಷಗಳಿಗೆ ಅಂದಾಜುಪಟ್ಟಿಯನ್ನು ತಯಾರಿಸಲಾಗಿದ್ದು, ಸದರಿ ಅಂದಾಜು ಪಟ್ಟಿಗೆ ಮಾನ್ಯ ಆಯುಕ್ತರವರು ಅಧಿಕಾರ ಪ್ರತ್ಯಾಯೋಜಿಸಿ ಹೊರಡಿಸಿರುವ ಆದೇಶ ಸಂಖ್ಯೆ :ಬಿ12(1) ಪಿ.ಆರ್/394/2023–24 ದಿನಾಂಕ: 06–12–2023 ರಂತೆ ನೀಡಿರುವ ಅಧಿಕಾರದನ್ವಯ ವಲಯ ಆಯುಕ್ತರು (ಯಲಹಂಕ)ರವರು ಕಂಡಿಕೆ(08)ರಲ್ಲಿ ಆಡಳಿತಾತ್ಮಕ ಅನುಮೋದನೆ ನೀಡಿರುತ್ತಾರೆ. ಅದರಂತೆ ಆಡಳಿತಾತ್ಮಕ ಅನುಮೋದನೆ ಟಿಪ್ಪಣಿಗೆ ಸಹಿ ಮಾಡಿದೆ. ಹಾಗೂ ಸದರಿ ಕಾಮಗಾರಿಗೆ ಟೆಂಡರ್ ಆಹ್ವಾನಿಸಬೇಕಾಗಿರುವುದರಿಂದ ತಾಂತ್ರಿಕ ಮಂಜೂರಾತಿ ಹಾಗೂ ಡಿ.ಟಿ.ಎಸ್. ಅನುಮೋದನೆ ನೀಡಲು ತಮ್ಮ ಮುಂದಿನ ಆದೇಶ ಕೋರಿ ಸಲ್ಲಿಸಿದೆ.

27/03/2025

Executive Engineer
Bruhat Bengaluru Mahanagara Palike
Yelahanka, Division

(11) ಮುಖ್ಯ ಅಭಿಯಂತರರು (ಯಲಹಂಕ ವಲಯ)

ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು ಯಲಹಂಕ ವಿಭಾಗರವರ ವರದಿಯನ್ನು ತಮ್ಮ ಅವಗಾಹನೆಗೆ ತರುತ್ತಾ, Resurfacing of roads at Maruthinagara 3rd main 6th, 7th and 8th cross roads in Kempegowda ward no -01 ಕಾಮಗಾರಿಗೆ 2024–25ನೇ ಸಾಲಿನ ಪಾಲಿಕೆಯ ಆಯವ್ಯಯದಲ್ಲಿ ಲೆಕ್ಕಶೀರ್ಷಿಕೆ ಪಿ–05–330502ರಡಿಯಲ್ಲಿ ರೂ.50.00ಲಕ್ಷಗಳಿಗೆ ಅನುದಾನ ಮಂಜೂರಾಗಿದ್ದು, ಕ್ರಿಯಾಯೋಜನೆಗೆ ಮಾನ್ಯ ಆಡಳಿತಗಾರರ ಅನುಮೋದನೆ ಪಡೆದು ಲೋಕೋಪಯೋಗಿ ಇಲಾಖೆಯ 2023–24ನೇ ಸಾಲಿನ ದರಪಟ್ಟಿಯಂತೆ ಅಂದಾಜುಪಟ್ಟಿ ತಯಾರಿಸಿ ಆಡಳಿತಾತ್ಮಕ ಅನುಮೋದನೆ ದೊರೆತಿದ್ದು, ಮಾನ್ಯ ಮುಖ್ಯ ಆಯುಕ್ತರ ಕಛೇರಿ ಆದೇಶ ಸಂಖ್ಯೆ:ಬಿ12(1)ಪಿಆರ್/394/2023–24, ದಿನಾಂಕ:06–12–2023 ರಂತೆ ಅಂದಾಜುಪಟ್ಟಿಗೆ ತಾಂತ್ರಿಕ ಮಂಜೂರಾತಿ ಮತ್ತು ಡಿಟಿಎಸ್ ಅನುಮೋದನೆ ಕೋರಿ ಕಡತವನ್ನು ತಮ್ಮ ಮುಂದಿನ ಆದೇಶಕ್ಕಾಗಿ ಸಲ್ಲಿಸಿದೆ.

ತಾಂತ್ರಿಕ ಸಹಾಯಕರು

(12) ಮುಖ್ಯ ಅಭಿಯಂತರರು (ಯ.ವ)

ಮುಖ್ಯ ಅಭಿಯಂತರರು
ಯಲಹಂಕ ವಲಯ
ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ

ಪು.ತಿ.ನೋ

ಪುಟದ ಸಂಖ್ಯೆ .....-04-

ಕಂಡಿಕೆ ಸಂಖ್ಯೆ | ಟಪ್ಪಣಿಗಳು ಮತ್ತು ಆಜ್ಞೆಗಳು

ಮಂಡಿಸಿದೆ.

ವಿಷಯ:- Resurfacing of roads at Maruthinagara 3rd main 6th, 7th and 8th cross roads in Kempegowda ward no -01. ಎಂಬ ಕಾಮಗಾರಿಯ ಟೆಂಡರ್ ಮೌಲ್ಯಮಾಪನದ ಬಗ್ಗೆ.

ಉಲ್ಲೇಖ:

1. ಕಾಮಗಾರಿ ಟೆಂಡರ್ ಪ್ರಕಟಣೆ ಸಂಖ್ಯೆ: BBMP/EE/YNK.D/KPPP/16/2024-25 dated:10-03-2025.

(12) * * * * *

ಮೇಲ್ಕಂಡ ವಿಷಯಕ್ಕೆ ಸಂಬಂದಿಸಿದಂತೆ, ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ ವ್ಯಾಪ್ತಿಯ ಪ್ರದೇಶಗಳಲ್ಲಿ ಮೂಲಭೂತ ಸೌಕಾರ್ಯಗಳ ಅಭಿವೃದ್ಧಿಗಾಗಿ 2024-25ನೇ ಸಾಲಿನ ಆಯವ್ಯಯದ ಲೆಕ್ಕಶೀರ್ಷಿಕೆ :05-330502ಅಡಿ ಹಿಂದುಳಿದ ವರ್ಗಗಳ ಕಲ್ಯಾಣ ನಿಧಿ ಅನುದಾನದಡಿಯಲ್ಲಿ ವಾರ್ಡ್‌ನಂ-01 ರ ವ್ಯಾಪ್ತಿಯ ಮಾರುತಿನಗರದ 3ನೇ ಮುಖ್ಯರಸ್ತೆ ಮತ್ತು 6ನೇ, 7ನೇ ಮತ್ತು 8ನೇ ರಸ್ತೆಗಳನ್ನು ಅಭಿವೃದ್ಧಿಪಡಿಸುವ ಕಾಮಗಾರಿಯ ವಿವರ ಈ ಕೆಳಕಂಡಂತಿದೆ.

Sl No	Name of work	Estimate cost Rs in Lakhs
01	Resurfacing of roads at Maruthinagara 3rd main 6th, 7th and 8th cross roads in Kempegowda ward no -01.	50.00
	Total	50.00

(13) ಈ ಮೇಲ್ಕಂಡ ಕಾಮಗಾರಿಗೆ ಮಾನ್ಯ ಮುಖ್ಯ ಅಭಿಯಂತರರು ಯಲಹಂಕ ವಲಯರವರಿಂದ ಅನುಮೊದನೆ ಪಡೆಯಲಾಗಿರುತ್ತದೆ. ಸದರಿ ಕಾಮಗಾರಿಗೆ 2023-24ನೇ ಸಾಲಿನ ಲೋಕೋಪಯೋಗಿ ಇಲಾಖೆ ದರಪಟ್ಟಿಯ ದರಗಳನ್ನು ಅನುಸರಿಸಿ ರೂ.50.00 ಲಕ್ಷಗಳಿಗೆ ಅಂದಾಜು ಪಟ್ಟಿಯನ್ನು ತಯಾರಿಸಿದ್ದು, ವಲಯ ಆಯುಕ್ತರು, ಯಲಹಂಕ ವಲಯರವರು ಆಡಳಿತಾತ್ಮಕ ಅನುಮೋದನೆ ನೀಡಿರುತ್ತಾರೆ. ಹಾಗೂ ಮುಖ್ಯ ಅಭಿಯಂತರರು, ಯಲಹಂಕ ವಲಯರವರು ತಾಂತ್ರಿಕ ಮಂಜೂರಾತಿ ಸಂಖ್ಯೆ ಬೃ.ಬೆಂ.ಮ.ಪಾ/ಮು.ಅ/ತಾ.ಮಂ/ಯ.ವ./ಪಿ.ಆರ್/2024-25 ದಿನಾಂಕ:_____ ರಂತೆ ತಾಂತ್ರಿಕ ಮಂಜೂರಾತಿಯನ್ನು ಮತ್ತು ಕರಡು ಟೆಂಡರ್ ಶೆಡ್ಯೂಲ್ - ಬಿ ಗೆ ಅನುಮೋದನೆ ನೀಡಿರುತ್ತಾರೆ.

(14) ಈ ಮೇಲ್ಕಂಡ ಕಾಮಗಾರಿಗೆ ಸಂಬಂದಿಸಿದಂತೆ ಉಲ್ಲೇಖ (1) ರಂತೆ ದಿನಾಂಕ: 10-03-2025 ರಂದು KTPP.Act and KW-04 Standard Tender Document ಅನುಸಾರ Karnataka Public procurement portal ಮುಖಾಂತರ ಟೆಂಡರ್ ಕರೆದಿದ್ದು, ಸದರಿ ಟೆಂಡರ್ ಪ್ರಕಟಣೆಯನ್ನು ಸಾರ್ವಜನಿಕ ಸಂಪರ್ಕಾಧಿಕಾರಿಗಳ ಮುಖಾಂತರ ಪ್ರಜಾವಾಣಿ ದಿನಪತ್ರಿಯಲ್ಲಿ ದಿನಾಂಕ:11-03-2025 ರಂದು ಪ್ರಕಟಿಸಲಾಗಿರುತ್ತದೆ.

ಸದರಿ ಟೆಂಡರ್‌ನ ವಿವರಗಳು ಈ ಕೆಳಕಂಡತಿರುತ್ತದೆ.

(15)

ಕ್ರ.ಸಂ	ಅಂಶಗಳು	ವಿವರಗಳು
1	ಕೆಲಸದ ಹೆಸರು	Resurfacing of roads at Maruthinagara 3rd main 6th, 7th and 8th cross roads in Kempegowda ward no -01.
2	ಅಂದಾಜು ಮೊತ್ತ	ರೂ. 50.00 ಲಕ್ಷಗಳು

ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ

ಟಿಪ್ಪಣಿ ಹಾಳೆ

ವಿಷಯ Re-Surfacing of roads at Maruthinagara 3rd main, 6th, 8th & 8th Cross roads in ward No-01

ಪುಟದ ಸಂಖ್ಯೆ -05-

ಕಡತದ ಸಂಖ್ಯೆ

ಕಂಡಿಕೆ ಸಂಖ್ಯೆ	ಟಿಪ್ಪಣಿಗಳು ಮತ್ತು ಆಜ್ಞೆಗಳು

(16)

3	ಇಂಡೆಂಟ್ ನಂ	BBMP/2024-25/OW/WORK_INDENT6868
4	ಅನುದಾನದ ಯೋಜನೆ ಹೆಸರು	2024–25 ನೇ ಸಾಲಿನ ಆಯವ್ಯಯದ ಅನುದಾನ
5	ಲೆಕ್ಕಶೀರ್ಷಿಕೆ	05–330502 ಅಡಿಯಲ್ಲಿ
6	ಅಡಳಿತಾತ್ಮಕ ಅನುಮೋದನೆ	ವಲಯ ಆಯುಕ್ತರು, ಯಲಹಂಕ ವಲಯರವರಿಂದ ಪಡೆಯಲಾಗಿರುತ್ತದೆ
7	ತಾಂತ್ರಿಕ ಮಂಜೂರಾತಿ ಮೊತ್ತ	ರೂ.50.00 ಲಕ್ಷಗಳು
8	ತಾಂತ್ರಿಕ ಮಂಜೂರಾತಿ ಸಂಖ್ಯೆ	ಸಂಖ್ಯೆ.ಬೃ.ಬೆಂ.ಮ.ಪಾ/ಮು.ಅ/ಯವ/ತಾ.ಮಂ/167 2024–25 ದಿನಾಂಕ: 07/03/2025 ರಂತೆ
9	ಟೆಂಡರ್‌ಗೆ ಇಟ್ಟ ಮೊತ್ತ	ರೂ. 42.35 ಲಕ್ಷಗಳು
10	ಅನ್ ಲೈನ್ Karnataka Public procurement portal ಮುಖಾಂತರ ಟೆಂಡರ್ ಸಲ್ಲಿಸಲು ಕೊನೆಯ ದಿನಾಂಕ	24-03-2025 upto 16.00 hrs
11	ಅನ್ ಲೈನ್ Karnataka Public procurement portal ಮುಖಾಂತರ ಟೆಂಡರ್ ತೆರೆಯುವ ದಿನಾಂಕ	25-03-2025 after 16.00 hrs

(17) ಮೇಲ್ಕಂಡ ಟೆಂಡರ್ ಪ್ರಕಟಣೆಗೆ ಸಂಬಂದಿಸಿದಂತೆ ದಿನಾಂಕ:25–03–2025 ರಂದು ಟೆಂಡರ್‌ಅನ್ನು ತೆರೆಯಲಾಗಿದ್ದು, ಸದರಿ ಟೆಂಡರ್‌ನಲ್ಲಿ ಇಬ್ಬರು ಗುತ್ತಿಗೆದಾರರು ಭಾಗವಹಿಸಿದ್ದು, ಗುತ್ತಿಗೆದಾರರ ವಿವರಗಳು ಈ ಕೆಳಕಂಡಂತಿರುತ್ತದೆ.

1. Sri. B.R.MOHAN
2. Sri. ANJAN KUMAR Y A

ಮೇಲ್ಕಂಡ ಗುತ್ತಿಗೆದಾರರು Karnataka Public procurement portalನಲ್ಲಿ ಭಾಗವಹಿಸಿದ್ದು, 1) Sri. B.R.MOHAN and 2) ANJAN KUMAR Y A ರವರ ದಾಖಲಾತಿಗಳನ್ನು ಪರಿಶೀಲಿಸಲಾಗಿ ಗುತ್ತಿಗೆದಾರರು ಕಾಮಗಾರಿ ದೃಢೀಕರಣ ಪತ್ರ, ಬ್ಯಾಂಕ್ ಗ್ಯಾರಂಟಿ, ಟರ್ನ್‌ಓವರ್ ಸರ್ಟಿಪೀಕೇಟ್ ಹಾಗೂ ಇತರೆ ಅವಶ್ಯಕವಾಗಿರುವ ಎಲ್ಲಾ ದಾಖಲಾತಿಗಳನ್ನು ಸಂಬಂಧಪಟ್ಟ ಕಛೇರಿಗಳಿಂದ ದೃಢೀಕರಿಸಿಕೊಳ್ಳಲಾಗಿದೆ. 'KW- Standard Tender Document ಅನುಸಾರ ನಿಗದಿಪಡಿಸಿರುವ ಎಲ್ಲಾ ಷರತ್ತುಗಳಂತೆ ತಾಂತ್ರಿಕ ಮೌಲ್ಯ ಮಾಪನದಲ್ಲಿ ಅರ್ಹತೆ ಹೊಂದಿರುತ್ತಾರೆ. ತಾಂತ್ರಿಕ ಮೌಲ್ಯಮಾಪನದ ವಿವರಗಳು ಮತ್ತು ತುಲನಾತ್ಮಕ ಪಟ್ಟಿಯನ್ನು ಕಡತದಲ್ಲಿ ಲಗತ್ತಿಸಿದೆ.

(18) ಮೇಲಿನ ವಿವರಗಳನ್ನು ತಮ್ಮ ಅವಗಾಹನೆಗೆ ತರುತ್ತಾ ಸದರಿ ಟೆಂಡರ್ ಪ್ರಕ್ರಿಯೆಯಲ್ಲಿ ಭಾಗವಹಿಸಿ ತಾಂತ್ರಿಕ ಮೌಲ್ಯಮಾಪನದಲ್ಲಿ ಅರ್ಹತೆ ಹೊಂದಿರುವ ಬಿಡ್‌ದಾರರಾದ 1) Sri. B.R.MOHAN and 2) ANJAN KUMAR Y A ರವರ ತಾಂತ್ರಿಕ ಬಿಡ್‌ನ್ನು ಅನುಮೋದಿಸಲು ಕೋರಿ ಕಡತವನ್ನು ತಮ್ಮ ಮುಂದಿನ ಆದೇಶಕ್ಕಾಗಿ ಮಂಡಿಸಿದೆ.

28/03/2025

ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಯಲಹಂಕ ವಿಭಾಗ

ಟಿಪ್ಪಣಿಗಳು ಮತ್ತು ಆಜ್ಞೆಗಳು

(19) ಮುಖ್ಯ ಅಭಿಯಂತರರು (ಯಲಹಂಕ ವಲಯ)

ಮುಖ್ಯ ಅಭಿಯಂತರರು
ಯಲಹಂಕ ವಲಯ
ಬೃಪತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ

(20) ಕಾ.ಪಾ.ಅ[ಯ.ವಿ]

ಯಲಹಂಕ ವಿಭಾಗದ ವ್ಯಾಪ್ತಿಯ ಸಂಖ್ಯೆ:01ರಲ್ಲಿ 2024-25ನೇ ಸಾಲಿನ ಆಯವ್ಯಯದ ಲೆಕ್ಕಶೀರ್ಷಿಕೆ:05-330502 ಅನುದಾನದಡಿಯಲ್ಲಿ ಸದರಿ ಕಾಮಗಾರಿಯನ್ನು ಕೈಗೊಂಡು ನಿರ್ವಹಿಸಲು ಒಟ್ಟು ಅಂದಾಜು ಮೊತ್ತ ರೂ.50.00 ಲಕ್ಷಗಳಿಗೆ ದಿನಾಂಕ:10-03-2025 ರಂದು ದ್ವಿ-ಲಕೋಟೆ ಪದ್ಧತಿಯಲ್ಲಿ Karnataka Public procurement portal ಮುಖಾಂತರ ಟೆಂಡರ್ ಕರೆಯಲಾಗಿರುತ್ತದೆ.

(21) ಸದರಿ ಟೆಂಡರ್‌ನಲ್ಲಿ ಇಬ್ಬರು ಗುತ್ತಿಗೆದಾರರಾದ 1) Sri. B.R.MOHAN and 2) ANJAN KUMAR Y A ರವರು ಭಾಗವಹಿಸಿ ಟೆಂಡರ್‌ನಲ್ಲಿ ನಿಗಧಿಪಡಿಸಿದ ಷರತ್ತುಗಳಂತೆ ಅರ್ಹ ದಾಖಿಲಾತಿಗಳನ್ನು ಸಲ್ಲಿಸಿರುತ್ತಾರೆ. ಸದರಿ ಗುತ್ತಿಗೆದಾರರು ತಾಂತ್ರಿಕವಾಗಿ ಅರ್ಹತೆ ಹೊಂದಿರುವುದರಿಂದ ಸದರಿಯವರ ತಾಂತ್ರಿಕ ಬಿಡ್‌ಅನ್ನು ಅನುಮೋದಿಸಿ ಆರ್ಥಿಕ ಬಿಡ್‌ಅನ್ನು ತೆರೆಯಲು ಮುಖ್ಯ ಅಭಿಯಂತರರು ಯಲಹಂಕ ವಲಯರವರು ಕಂಡಿಕೆ(19)ರಲ್ಲಿ ಅನುಮೋದನೆ ನೀಡಿರುತ್ತಾರೆ. ಅದರಂತೆ ತಾಂತ್ರಿಕವಾಗಿ ಅರ್ಹರಾಗಿರುವ ಬಿಡ್ದುದಾರರ ಆರ್ಥಿಕ ಬಿಡ್‌ಅನ್ನು ತೆರೆಯಲಾಗಿದ್ದು,

ವಿವರ ಈ ಕೆಳಕಂಡಂತಿರುತ್ತದೆ.

ಕ್ರ. ಸಂ	ಗುತ್ತಿಗೆದಾರರ ಹೆಸರು	ಟೆಂಡರ್ ಗಿಟ್ಟ ಮೊತ್ತ 2023-24ನೇ ಸಾಲಿನ ಅನುಮೋದಿತ ದರಗಳಿಗೆ ಹೊಲಿಸಿದಾಗ.	ಗುತ್ತಿಗೆ ದಾರರು ನಮೂದಿಸಿರುವ ದರಗಳು	2023-24ನೇ ಸಾಲಿನ ದರಗಳಿಗೆ ಹೋಲಿಸಿದಾಗ ಕಡಿಮೆ ವಾರು	ಷರಾ
01	B.R.MOHAN	4235686.29	4362324.16	(+)2.99% ಹೆಚ್ಚು	
02	ANJAN KUMAR.Y A		4383935.21	(+)3.50% ಹೆಚ್ಚು	

(22) ಮೇಲ್ಕಂಡ ಗುತ್ತಿಗೆದಾರರು ಸಲ್ಲಿಸಿರುವ ಆರ್ಥಿಕ ಬಿಡ್‌ಅನ್ನು ಪರಿಶೀಲಿಸಿ **SRI** B.R.MOHAN ರವರು ನಮೂದಿಸಿರುವ **ರೂ. 43,62,324.16**ಗಳು ಅತಿ ಕಡಿಮೆ ದರಗಳಾಗಿರುತ್ತದೆ.

ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ

ಟಿಪ್ಪಣಿ ಹಾಳೆ

ವಿಷಯ Re-surfacing of roads at maruthi nagar 3rd main, 6th, 9th, 8th Cross roads in Ward No-01 ಪುಟದ ಸಂಖ್ಯೆ -07-

ಕಡತದ ಸಂಖ್ಯೆ

ಕಂಡಿಕೆ ಸಂಖ್ಯೆ	ಟಿಪ್ಪಣಿಗಳು ಮತ್ತು ಆಜ್ಞೆಗಳು
(23)	ಆದುದರಿಂದ ಗುತ್ತಿಗೆದಾರರಾದ **SRI B.R.MOHAN** ರವರು ನಮೂದಿಸಿರುವ ರೂ. **43,62,324.16** ಗಳು ಅತಿ ಕಡಿಮೆ ದರಗಳಾಗಿದ್ದು, ಅನುಮೋದಿತ ಅಂದಾಜು ಪಟ್ಟಿಯ 2023-24ನೇ ಸಾಲಿನ ದರಗಳ ದರಪಟ್ಟಿಗೆ ಹೋಲಿಸಿದಾಗ ಶೇಕಡ (+)2.99% ರಷ್ಟು ಹೆಚ್ಚಾಗಿರುತ್ತದೆ. ಆದುದರಿಂದ ಸದರಿ ಟೆಂಡರ್‌ನಲ್ಲಿ ಅರ್ಹ ಗುತ್ತಿಗೆದಾರರಾದ **SRI B.R.MOHAN** ರವರು ನಮೂದಿಸಿರುವ ದರ **ರೂ.43,62,324.16**ಗಳಿಗೆ ಅನುಮೋದನೆ ನೀಡಲು ಕೋರಿ ಕಡತವನ್ನು ತಮ್ಮ ಮುಂದಿನ ಆದೇಶಕ್ಕಾಗಿ ಮಂಡಿಸಿದೆ. 29 MAR 2025 547 ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು ಯಲಹಂಕ ವಿಭಾಗ 29/03/2025
(24)	ಮುಖ್ಯ ಅಭಿಯಂತರರು (ಯಲಹಂಕ ವಲಯ) ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು ಯಲಹಂಕ ವಿಭಾಗರವರ ವರದಿಯನ್ನು ತಮ್ಮ ಅವಗಾಹನೆಗೆ ತರುತ್ತಾ, ತಾಂತ್ರಿಕ ಬಿಡ್‌ನಲ್ಲಿ ಅರ್ಹರಾದ ಇಬ್ಬರು ಬಿಡ್‌ದಾರರ ಆರ್ಥಿಕ ಬಿಡ್‌ನ್ನು ದಿನಾಂಕ:10-03-2025ರಂದು ತೆರೆಯಲಾಗಿದ್ದು ಅತಿ ಕಡಿಮೆ ದರ ನಮೂದಿಸಿರುವ ಎಲ್-1 ಬಿಡ್‌ದಾರರಾದ ಶ್ರೀ.ಬಿ.ಆರ್.ಮೋಹನ್‌ರವರ ದರ ರೂ.43,62,324.00ಗಳಾಗಿದ್ದು, ಟೆಂಡರ್‌ಗಿಟ್ಟ ಮೊತ್ತಕ್ಕೆ ತುಲನೆ ಮಾಡಿದಾಗ ಶೇಕಡ(+)2.99%ರಷ್ಟು ಹೆಚ್ಚು ದರಗಳಾಗಿರುತ್ತದೆ. ಮಾನ್ಯ ಮುಖ್ಯ ಆಯುಕ್ತರ ಕಛೇರಿ ಆದೇಶ ಸಂಖ್ಯೆ:ಬಿ12(1)ಪಿಆರ್/394/2023-24 ದಿನಾಂಕ:06-12-2023ರಂತೆ ಟೆಂಡರ್ ಅನುಮೋದನೆಗೆ ಮಾನ್ಯ ವಲಯ ಆಯುಕ್ತರು, ಯಲಹಂಕ ವಲಯ ರವರಿಗೆ ಸಲ್ಲಿಸಲು ತಮ್ಮ ಮುಂದಿನ ಆದೇಶಕ್ಕೆ ಸಲ್ಲಿಸಿದೆ. ತಾಂತ್ರಿಕ ಸಹಾಯಕರು
(25)	ಮುಖ್ಯ ಅಭಿಯಂತರರು (ಯ.ವ) ಕಂಡಿಕೆ(21)ರಿಂದ(23)ರವರೆಗಿನ ವರದಿಯಂತೆ ಎಲ್-1 ಬಿಡ್‌ದಾರರಾದ ಶ್ರೀ.ಬಿ.ಆರ್.ಮೋಹನ್‌ರವರು ನಮೂದಿಸಿರುವ ದರ ಮೊತ್ತ ರೂ.43,62,324.00ಗಳು ಟೆಂಡರ್‌ಗಿಟ್ಟ ಮೊತ್ತಕ್ಕೆ ತುಲನೆ ಮಾಡಿದಾಗ ಶೇಕಡ(+)2.99%ರಷ್ಟು ಹೆಚ್ಚು ದರಗಳಿಗೆ ಟೆಂಡರ್ ಅನುಮೋದನೆ ಕೋರಿ ಮಂಡಿಸಿದೆ. ಮುಖ್ಯ ಅಭಿಯಂತರರು (ಯ.ವ) ಯಲಹಂಕ ವಲಯ ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ
(26)	ಮಾನ್ಯ ವಲಯ ಆಯುಕ್ತರು (EE, Yelahanka) ಅನುಮೋದಿಸಿದೆ ವಲಯ ಆಯುಕ್ತರು ಯಲಹಂಕ ವಲಯ ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ ಬ್ಯಾಟರಾಯನಪುರ, ಬೆಂಗಳೂರು-92.

ಮುಖ್ಯ ಅಭಿಯಂತರರು ಯಲಹಂಕ ವಲಯ, ಜಿಬಿಬಿಪಿ ಕಛೇರಿ ಆವರಣ, ಬ್ಯಾಟರಾಯನಪುರ, ಬೆಂಗಳೂರು-92 ದಿನಾಂಕ: 29/4/25

ಕಂಡಿಕೆ ಸಂಖ್ಯೆ	ಪುಟದ ಸಂಖ್ಯೆ ..... — 14 — ಕಡತದ ಸಂಖ್ಯೆ ..... ಟಪ್ಪಣಿಗಳು ಮತ್ತು ಆಜ್ಞೆಗಳು

(24) 2024–25ನೇ ಸಾಲಿನ ಆಯವ್ಯಯದ ಲೆಕ್ಕಶೀರ್ಷಿಕೆ:05–330502ರ ಅನುದಾನದಲ್ಲಿ ಮಂಜೂರಾಗಿರುವ ಕಾಮಗಾರಿಯಾದ "Resurfacing of roads at Maruthinagara 3rd main 6th, 7th and 8th cross roads in Kempegowda ward no -01" ಎಂಬ ಕಾಮಗಾರಿಗೆ ಟೆಂಡರ್ ಅನುಮೋದನೆ ಕೋರಿ ವಲಯ ಆಯುಕ್ತರು (ಯಲಹಂಕ ವಲಯ), ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ ರವರಿಗೆ ಕಂಡಿಕೆ( ) ರಲ್ಲಿ ಪ್ರಸ್ತಾವನೆ ಸಲ್ಲಿಸಲಾಗಿತ್ತು. ಅದರಂತೆ ವಲಯ ಆಯುಕ್ತರು, (ಯಲಹಂಕ ವಲಯ) ರವರು ಗುತ್ತಿಗೆದಾರರಾದ VINAYAKA ENTERPRISES, Prop B.R.Mohan ರವರ ಟೆಂಡರ್ ಅನುಮೋದನೆಯ ಮೊತ್ತವಾದ Rs.43,62,324/- ಗಳಿಗೆ ಅನುಮೋದನೆ ನೀಡಿರುತ್ತಾರೆ. ಅದರಂತೆ ಸದರಿ ಮೊತ್ತಕ್ಕೆ ಶೇಕಡ 5% ರಷ್ಟು ಎಫ್.ಎಸ್.ಡಿ (Performance security) ಹಾಗೂ ರೂ.2500/–ಗಳ Stamp Paper ನೀಡುವಂತೆ Letter of Acceptence ತಯಾರಿಸಿ ಸಹಿ ಮಾಡಿದೆ.

ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು,
ಯಲಹಂಕ ವಿಭಾಗ

(25) ಕಂಡಿಕೆ ಮುಂದುವರೆದಂತೆ ಸರ್ಕಾರದ ಆದೇಶ ಸಂಖ್ಯೆ: FD 20 CSL 2022 Dated: 15-07-2022 and ಸಂಖ್ಯೆ:ಆಇ 447 ವೆಚ್ಚ–12/2022 ದಿನಾಂಕ: 30–07–2022 ರಂತೆ ಟೆಂಡರ್ ಮೊತ್ತಕ್ಕೆ ಶೇಕಡ +18% GST Charges Amount Rs.7,85,284/-ಗಳನ್ನು ಸೇರಿಸಿ ಒಟ್ಟು ಮೊತ್ತ Rs.51,47,542/- ಗಳಾಗಿದ್ದು ಸರ್ಕಾರಿ ಆದೇಶ ಸಂಖ್ಯೆ: ಅಇ876(P-1)ವೆಚ್ಚ–12–17 ದಿನಾಂಕ:12–10–2017 ಆದೇಶದಂತೆ ಕೆಟಿಪಿಪಿ ಕಾಯ್ದೆ 2000ರ ನಿಯಮ 27ಎ ರಡಿ ಪರಿಶಿಷ್ಟ ಜಾತಿ ಮತ್ತು ಪರಿಶಿಷ್ಟ ಪಂಗಡದವರಿಗೆ ಭದ್ರತಾ ಠೇವಣಿ ಮೊತ್ತವನ್ನು ಕಾಮಗಾರಿಯ ಬಿಲ್ಲು ಪಾವತಿಸುವ ಸಮಯದಲ್ಲಿ ಕಟಾವು ಮಾಡಲು ಆದೇಶಿಸಿರುತ್ತಾರೆ. ಅದರಂತೆ ಗುತ್ತಿಗೆದಾರರಾದ VINAYAKA ENTERPRISES, Prop B.R.Mohan ರವರೊಂದಿಗೆ ಕರಾರು ಒಡಂಬಡಿಕೆ ಮಾಡಿಕೊಂಡು ಅನ್‌ಲೈನ್ ಮೂಲಕ ಕಾರ್ಯಾದೇಶ (Work Order) ನೀಡಲಾಗಿದೆ.

26/05/25

ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು,
ಯಲಹಂಕ ವಿಭಾಗ

ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ

ಟಿಪ್ಪಣಿ ಹಾಳೆ

ಸ.ಕಾ.ಅ/ಯ.ಉ.ವಿ. ಸ.ಕಾ.ಅ. ಸಂಖ್ಯೆ: 021 ದಿನಾಂಕ: 31-2-2025

ವಿಷಯ ..... ಪುಟದ ಸಂಖ್ಯೆ .....01.....

..... ಕಡತದ ಸಂಖ್ಯೆ .....

ಕಂಡಿಕೆ ಸಂಖ್ಯೆ	ಟಿಪ್ಪಣಿಗಳು ಮತ್ತು ಆಜ್ಞೆಗಳು	YNK-DBR No. Date.

ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು, ಯಲಹಂಕ ವಿಭಾಗ ರವರಿಗೆ ಮಂಡಿಸಿದೆ.

ವಿಷಯ:– Resurfacing of roads at Maruthinagara 3rd Main, 6th, 7th and 8th cross roads in Kempegowda ward no:01

ಉಲ್ಲೇಖ:– EE/YNK.D/WO/KPPP-16/WO/14/2025-26, dt:26/05/2025

******

ಮೇಲ್ಕಂಡ ವಿಷಯಕ್ಕೆ ಸಂಬಂಧಿಸಿದಂತೆ ಹಾಗೂ ಉಲ್ಲೇಖ (1) ರಂತೆ ಕಾಮಗಾರಿ ಆದೇಶವನ್ನು **Sri.Vinayaka Enterprises Prop.B.R.Mohan** ಗುತ್ತಿಗೆದಾರರಿಗೆ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು, ಯಲಹಂಕ ವಿಭಾಗ ರವರು ನೀಡಿರುತ್ತಾರೆ. ಗುತ್ತಿಗೆದಾರರು ಕಾಮಗಾರಿಯನ್ನು ಸಮರ್ಪಕವಾಗಿ ನಿರ್ವಹಿಸಿದ್ದು, ಕಾಮಗಾರಿಗೆ ಸಂಬಂಧಿಸಿದಂತೆ **1st and Final Bill** ಬಿಲ್ಲನ್ನು ₹ 43,59,601. ಗಳಿಗೆ ತಯಾರಿಸಿ ಅಳತೆಗಳನ್ನು ಅಳತೆ ಪುಸ್ತಕ ಸಂಖ್ಯೆ: 1304 ಪುಟ ಸಂಖ್ಯೆ: 130361 ರಿಂದ 130365 ರಲ್ಲಿ ನಮೂದಿಸಿ ಬಿಲ್ ಪಾವತಿಗಾಗಿ ಕಡತವನ್ನು ಸಲ್ಲಿಸಿದೆ.

31/2/2025

ಸ.ಕಾ.ಅ),

ಕಂಡಿಕೆ (1) ರಲ್ಲಿ ತಿಳಿಸಿರುವಂತೆ ಗುತ್ತಿಗೆದಾರರಾದ **Sri.Vinayaka Enterprises Prop.B.R.Mohan** ಗುತ್ತಿಗೆದಾರರಿಗೆ ಮೇಲಿನ ಕೆಲಸವನ್ನು ಸಮರ್ಪಕವಾಗಿ ಪೂರ್ಣಗೊಳಿಸಿರುತ್ತಾರೆ. ಆದ್ದರಿಂದ ಗುತ್ತಿಗೆದಾರರಿಗೆ **1st and Final Bill** ಬಿಲ್ಲನ್ನು ತಯಾರಿಸಿ ರೂ. 43,59,601 ಗಳನ್ನು ಪಾವತಿಸಲು ಕಡತವನ್ನು ತಮ್ಮ ಮುಂದಿನ ಆದೇಶಕ್ಕೆ ಮಂಡಿಸಿದೆ.

Asst. Executive Engineer
Yelahanka Division
(BBMP Yelahanka Zn)
Yelahanka, Bangalore

Executive Engineer (YNK)

ಪು.ತಿ.ನೋ

ಕಂಡಿಕೆ ಸಂಖ್ಯೆ	ಪುಟದ ಸಂಖ್ಯೆ 02 ಕಡತದ ಸಂಖ್ಯೆ ಟಿಪ್ಪಣಿಗಳು ಮತ್ತು ಆಜ್ಞೆಗಳು

ಸದರಿ ಕಾಮಗಾರಿಯನ್ನು ಗುತ್ತಿಗೆದಾರರಾದ B.R.MOHAN ರವರು ನಿರ್ವಹಿಸಿ ಪೂರೈಸಿದ್ದು, ಕಾಮಗಾರಿಯ 1st & Final ಬಿಲ್ಲಿನ

34) ಅಳತೆಗಳನ್ನು ಅಳತೆ ಪುಸ್ತಕ ಸಂಖ್ಯೆ-------- ಪುಟ ಸಂಖ್ಯೆ:---------- ರಿಂದ ----------ರಲ್ಲಿ ದಾಖಲಿಸಿ ಸಹಾಯಕ ಅಭಿಯಂತರರು, ವಾರ್ಡ್---- ಮತ್ತು ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು, ಯಲಹಂಕ ಉಪವಿಭಾಗ / ಯಲಹಂಕ ಉಪನಗರ ಉಪವಿಭಾಗ ರವರು ಪಾವತಿಗಾಗಿ ಶಿಫಾರಸ್ಸು ಮಾಡಿರುತ್ತಾರೆ.

ಕೆ.ಎಫ್.ಸಿ ಕಾಯ್ದೆ ಪ್ರಕಾರ ಲೆಕ್ಕ ಪರಿಶೋಧನೆ ಮಾಡಿದ್ದು, ಬಿಲ್ಲಿನ ಒಟ್ಟು ಮೊತ್ತ ರೂ.5144330=00 ಗಳಿದ್ದು, ಇದರಲ್ಲಿ ಶಾಸನ ಬದ್ಧ ಕಟಾವಣೆ ಮೊತ್ತ

35) ರೂ:44428400 ಗಳನ್ನು ಕಟಾಯಿಸಿ ಉಳಿಕೆ ನಿವ್ವಳ ಮೊತ್ತ ರೂ.4700046=00 ಗಳನ್ನು ಗುತ್ತಿಗೆದಾರರಿಗೆ ಪಾವತಿಸಲು ಬಿಲ್ಲಿನ ವಿವರಗಳನ್ನು IFMS ತಂತ್ರಾಂಶದಲ್ಲಿ ಬಿ.ಆರ್.ದಾಖಲಿಸಿ ಕೇಂದ್ರ ಕಛೇರಿಗೆ ಸಲ್ಲಿಸಲು ಆದೇಶಕ್ಕಾಗಿ ಮಂಡಿಸಿದೆ. 31/7

36) 1.8.16

Executive Engineer
Bruhat Bengaluru Mahanagara Palike
Yelahanka, Division

ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ

ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರ ಕಛೇರಿ ಯಲಹಂಕ ವಿಭಾಗ

ದಿನಾಂಕ: 31/03/2025

"ಪ್ರಮಾಣ ಪತ್ರ"

ಕಾಮಗಾರಿಯ ಹೆಸರು	Resurfacing of roads at Maruthinagara 3rd main 6th, 7th and 8th cross roads in Kempegowda ward no:01
ಜಾಬ್ ಕೋಡ್ ಸಂಖ್ಯೆ	001-25-000019
ಕರಾರು ಒಪ್ಪಂದದ ಸಂಖ್ಯೆ ಮತ್ತು ದಿನಾಂಕ	EE/YNK/KPPP-16/AG/07/2025-26, dt:26/05/2025
ಕಾರ್ಯಾದೇಶ ಸಂಖ್ಯೆ ಮತ್ತು ದಿನಾಂಕ	BBMP/EE/YNK.D/KPPP-16/W.O/14/2025-26, dt:26/05/2025
ಕಾಮಗಾರಿಯ ಒಟ್ಟು ಅಂದಾಜು ಮೊತ್ತ ರೂ. ಲಕ್ಷಗಳಲ್ಲಿ	Rs.50.00 lakhs

****

ಮೇಲ್ಕಂಡ ಕಾಮಗಾರಿಯು ಲೋಕಾಯುಕ್ತ/ಸಿ.ಓ.ಡಿ/ಎ.ಸಿ.ಬಿ/ಪಾಲಿಕೆ ಅಥವಾ ಮತ್ಯಾವುದೇ ತನಿಖಾ ಸಂಸ್ಥೆಯ ತನಿಖೆಗೆ ಒಳಪಟ್ಟಿರುವ ಬಗ್ಗೆ ಈ ಕಛೇರಿಗೆ ಈ ದಿನದವರೆಗೂ ಯಾವುದೇ ಮಾಹಿತಿ ಸ್ವೀಕೃತವಾಗಿರುವುದಿಲ್ಲವೆಂದು ಈ ಮೂಲಕ ದೃಢೀಕರಿಸಲಾಗಿದೆ. ಹಾಗೂ ಸದರಿ ಕಾಮಗಾರಿಯ ಜಾಬ್‌ಕೋಡ್ 001-25-000019 ಅಂದಾಜು ಮೊತ್ತ ರೂ. 50.00 ಲಕ್ಷಗಳಾಗಿದ್ದು, ಸದರಿ ಕಾಮಗಾರಿಯ 1st & Final ಬಿಲ್ಲಿನ ಮೊತ್ತ ರೂ. 43,59,601 ಗಳನ್ನು ಪಾವತಿಸಲು ಆನ್‌ಲೈನ್ ಮೂಲಕ ಸಲ್ಲಿಸಲಾಗಿದೆ.

ಸಹಾಯಕ ಅಭಿಯಂತರರು
ವಾರ್ಡ್ ನಂ-01

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಯಲಹಂಕ ಉಪನಗರ ಉಪವಿಭಾಗ
ಬಿಬಿಎಂಪಿ ಬೆಂಗಳೂರು-560064

Assistant Executive Engineer
Yelahanka Sub Division
(BBMP Yelk. Zn)
Yelahanka, Bangalore

ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಯಲಹಂಕ ವಿಭಾಗ,
ಬಿಎಂಪಿ ಬೆಂಗಳೂರು-64

ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ

ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರ ಕಛೇರಿ ಯಲಹಂಕ ವಿಭಾಗ

ದಿನಾಂಕ: 31/07/2025

"ದೃಢೀಕರಣ ಪತ್ರ"

ಕಾಮಗಾರಿಯ ಹೆಸರು	Resurfacing of roads at Maruthinagara 3rd Main, 6th, 7th and 8th cross roads in Kempegowda ward no:01
ಜಾಬ್ ಕೋಡ್ ಸಂಖ್ಯೆ	001–25–000019
ಪಿ–ಕೋಡ್	3863
ಕರಾರು ಒಪ್ಪಂದ ಪತ್ರದ ಸಂಖ್ಯೆ ಮತ್ತು ದಿನಾಂಕ	EE/YNK/KPPP-16/AGD/2025-26, dt:26/05/2025
ಕಾರ್ಯಾದೇಶ ಸಂಖ್ಯೆ ಮತ್ತು ದಿನಾಂಕ	BBMP/EE/YNK.D/KPPP-16/W.O/14/2025-26, dt:26/05/2025
ಅಂದಾಜು ಮೊತ್ತ ರೂ.ಲಕ್ಷಗಳಲ್ಲಿ	50.00 Lakhs
ಬಿಲ್ಲಿನ ಮೊತ್ತ ರೂ /– (ಭಾಗಶಃ / ಅಂತಿಮ ಬಿಲ್ಲು)	43,59,601

****

ಮೇಲ್ಕಂಡಂತೆ ವಿವರಿಸಿರುವ ಕಾಮಗಾರಿಗೆ ಸಂಬಂಧಿಸಿದಂತೆ, ಸದರಿ ಕಾಮಗಾರಿಯು ಯಾವುದೇ ರೀತಿಯಲ್ಲಿ Overlap ಆಗಿರುವುದಾಗಲೀ ಅಥವಾ Duplication ಆಗಿರುವುದಾಗಲೀ ಆಗಿರುವುದಿಲ್ಲ, ಸದರಿ ಕಾಮಗಾರಿಯು ಇತರೆ ಯಾವುದೇ ಕಾಮಗಾರಿಯ DLP (Defect liability period) ಅವಧಿಯಲ್ಲಿ ಇಲ್ಲದಿರುವುದಾಗಿ ಹಾಗೂ ಸದರಿ ಕಾಮಗಾರಿಯನ್ನು ಬೇರೊಂದು ಕಾಮಗಾರಿ ಅಡಿಯಲ್ಲಿ ಅಥವಾ ಇತರೆ ಯಾವುದೇ ಅನುದಾನದಡಿಯಲ್ಲಿ ಕೈಗೊಳ್ಳಲು ಉದ್ದೇಶಿಸಿ ಕಾಮಗಾರಿಯನ್ನು ಕೈಗೊಂಡಿರುವುದಿಲ್ಲದಿರುವುದಾಗಿ ದೃಢೀಕರಿಸುತ್ತಾ, ಪ್ರಸ್ತುತ ಪಾವತಿಗೆ ಸಲ್ಲಿಸುತ್ತಿರುವ ಕಾಮಗಾರಿಯನ್ನು ಇದೇ ಕಾಮಗಾರಿ ಅಡಿಯಲ್ಲಿ, ಅಂದಾಜು ಪಟ್ಟಿಯಡಿಯಲ್ಲಿ ಹಾಗೂ ಇದೇ ಅನುದಾನದಡಿಯಲ್ಲಿ ಅನುಷ್ಠಾನಗೊಳಿಸಿರುವುದಾಗಿ ಈ ಮೂಲಕ ದೃಢೀಕರಿಸಿದೆ.

ಸಹಾಯಕ ಅಭಿಯಂತರರು
ವಾರ್ಡ್ ನಂ:01

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಯಲಹಂಕ ಉಪವಿಭಾಗ
ಬಿಬಿಎಂಪಿ ಬೆಂಗಳೂರು–560064
Velahanka, Bangalore

ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು,
ಯಲಹಂಕ ವಿಭಾಗ, ಬಿಬಿಎಂಪಿ, ಬೆಂಗಳೂರು–64

ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ

ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರ ಕಛೇರಿ ಯಲಹಂಕ ವಿಭಾಗ

ದಿನಾಂಕ: 31/07/25

"ದೃಢೀಕರಣ ಪತ್ರ"

ಕಾಮಗಾರಿಯ ಹೆಸರು	Resurfacing of roads at Maruthinagara 3rd Main, 6th, 7th and 8th cross roads in Kempegowda ward no:01
ಜಾಬ್ ಕೋಡ್ ಸಂಖ್ಯೆ	001–25–000019
ಪಿ–ಕೋಡ್	3813
ಕರಾರು ಒಪ್ಪಂದ ಪತ್ರದ ಸಂಖ್ಯೆ ಮತ್ತು ದಿನಾಂಕ	EE/YNK/KPPP-16/AG/07/2025-26, dt:26/05/2025
ಕಾರ್ಯಾದೇಶ ಸಂಖ್ಯೆ ಮತ್ತು ದಿನಾಂಕ	BBMP/EE/YNK.D/KPPP-16/W.O/14/2025-26, dt:26/05/2025
ಅಂದಾಜು ಮೊತ್ತ ರೂ.ಲಕ್ಷಗಳಲ್ಲಿ	50.00 Lakhs
ಬಿಲ್ಲಿನ ಮೊತ್ತ ರೂ /– (ಭಾಗಶಃ / ಅಂತಿಮ ಬಿಲ್ಲು)	43,59,601

****

ಮೇಲ್ಕಂಡ ನಾಮಾಂಕಿತದ ಕಾಮಗಾರಿಯ ಬಿಲ್ಲಿಗೆ ಸಂಬಂಧಿಸಿದ ಧೃಡೀಕೃತ ದಾಖಲೆಗಳನ್ನು **Financial code** ಪ್ರಕಾರ ಪರಿಶೀಲಿಸಿದ್ದು, **Pre-audit** ನಲ್ಲಿ ಯಾವುದೇ ನ್ಯೂನತೆ/ಲೋಪದೋಷಗಳು ಕಂಡು ಬಂದಿಲ್ಲದಿರುವುದು ಹಾಗೂ ಈ ಕಾಮಗಾರಿಯ ಬಿಲ್ಲಿಗೆ ಸಂಬಂಧಿಸಿದಂತೆ ತಹಲ್‌ವರೆಗೆ ಯಾವುದೇ ರೀತಿಯ **Audit objection** ಸಹ ಇಲ್ಲದಿರುವುದನ್ನು ಈ ಮೂಲಕ ದೃಡೀಕರಿಸಲಾಗಿದೆ.

31/7/25

ಲೆಕ್ಕ ಅಧೀಕ್ಷಕರು,
ಯಲಹಂಕ ವಿಭಾಗ,
ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ

ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ

ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರ ಕಛೇರಿ ಯಲಹಂಕ ವಿಭಾಗ

ದಿನಾಂಕ: 31/07/25

"ದೃಢೀಕರಣ ಪತ್ರ"

ಕಾಮಗಾರಿಯ ಹೆಸರು	Resurfacing of roads at Maruthinagara 3rd Main, 6th, 7th and 8th cross roads in Kempegowda ward no:01
ಜಾಬ್ ಕೋಡ್ ಸಂಖ್ಯೆ	001–25–000019
ಕರಾರು ಒಪ್ಪಂದ ಪತ್ರದ ಸಂಖ್ಯೆ ಮತ್ತು ದಿನಾಂಕ	EE/YNK/KPPP-16/AG/07/2025-26, dt:26/05/2025
ಕಾರ್ಯಾದೇಶ ಸಂಖ್ಯೆ ಮತ್ತು ದಿನಾಂಕ	BBMP/EE/YNK.D/KPPP-16/W.O/14/2025-26, dt:26/05/2025
ಅಂದಾಜು ಮೊತ್ತ ರೂ.ಲಕ್ಷಗಳಲ್ಲಿ	50.00 Lakhs
ಬಿಲ್ಲಿನ ಮೊತ್ತ	43,59,601

****

ಮೇಲ್ಕಂಡ ನಾಮಾಂಕಿತದ ಕಾಮಗಾರಿಯನ್ನು ಕೈಗೊಳ್ಳುವ ಸಂಬಂಧ ಅಂದಾಜು ಪಟ್ಟಿ ತಯಾರಿಕೆಯಿಂದ ಹಿಡಿದು ಗುಣಮಟ್ಟದ ಕಾಮಗಾರಿಯನ್ನು ಅನುಷ್ಠಾನಗೊಳಿಸುವ ಸಂಬಂಧದ ಎಲ್ಲಾ ಹಂತದ ಪ್ರಕ್ರಿಯೆಗಳನ್ನು ನಿಯಮಾನುಸಾರ ಅನುಸರಿಸಿ, ಸದರಿ ಕಾಮಗಾರಿಯನ್ನು ನಿಯಮಾನಸಾರ ಎಲ್ಲಾ ಹಂತದ ಪ್ರಕ್ರಿಯೆಗಳನ್ನು ಅನುಸರಿಸಿ ಅನುಷ್ಠಾನಗೊಳಿಸಲಾಗಿದ್ದು, ಅನುಷ್ಠಾನಗೊಳಿಸಿರುವ ಸಂಬಂಧ ಎಲ್ಲಾ ಅವಶ್ಯ ದಾಖಲಾತಿಗಳ ಜೊತೆಗೆ ಗುಣಮಟ್ಟ ಪ್ರಮಾಣ ಪತ್ರಗಳನ್ನು ದೃಢೀಕರಿಸಿ ಹಾಗೂ ನಿಜಸ್ಥಿತಿಯ ಅಳತೆಗಳನ್ನು ತೆಗೆದು ಇ-ಅಳತೆ ಪುಸ್ತಕದಲ್ಲಿ ದಾಖಲಿಸಿ ಸಂಬಂಧಪಟ್ಟ ಸಹಾಯಕ ಅಭಿಯಂತರರು ಮತ್ತು ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು 100% Check Measurement ಹಾಗೂ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು 25% Check Measurement ಗಳ ದಾಖಲಾತಿಗಳೊಂದಿಗೆ ಪಶ್ನಿತ ಕಾಮಗಾರಿಯು ಮೊದಲನೇ ಭಾಗಶಃ/ಎರಡನೇ ಭಾಗಶಃ ಸಂಪೂರ್ಣವಾಗಿ ಪೂರ್ಣಗೊಂಡಿರುವುದಾಗಿ ದೃಢೀಕರಿಸುತ್ತಾ, ಗುಣಮಟ್ಟ ಕಾಮಗಾರಿಯನ್ನು ಅನುಷ್ಠಾನಗೊಳಿಸಿರುವುದರಿಂದ ಕಾಮಗಾರಿಯ ಹಣ ಪಾವತಿಗೆ ಆನ್‌ಲೈನ್‌ನಲ್ಲಿ ಕಾಮಗಾರಿಯನ್ನು ಅನುಷ್ಠಾನಗೊಳಿಸಿದ ಎಲ್ಲಾ ದಾಖಲಾತಿಗಳನ್ನು ದೃಢೀಕರಿಸಿ ಅಫ್‌ಲೋಡ್ ಮಾಡುತ್ತಾ. ಸದರಿ ಕಾಮಗಾರಿಗೆ ಹಣ ಪಾವತಿ ಮಾಡಬಹುದಾಗಿರುತ್ತದೆ ಎಂದು ಈ ಮೂಲಕ ದೃಢೀಕರಿಸಿದೆ.

ಸಹಾಯಕ ಅಭಿಯಂತರರು
ವಾರ್ಡ್ ನಂ 01

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಯಲಹಂಕ ಉಪವಿಭಾಗ
ಬಿಬಿಎಂಪಿ ಬೆಂಗಳೂರು-560064

ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಯಲಹಂಕ ವಿಭಾಗ,
ಬಿಎಂಪಿ ಬೆಂಗಳೂರು-64

ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ

ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರ ಕಛೇರಿ ಯಲಹಂಕ ವಿಭಾಗ

ದಿನಾಂಕ: 31/03/25

"ದೃಢೀಕರಣ ಪತ್ರ"

ಕಾಮಗಾರಿಯ ಹೆಸರು	Resurfacing of roads at Maruthinagara 3rd Main, 6th, 7th and 8th cross roads in Kempegowda ward no:01
ಜಾಬ್ ಕೋಡ್ ಸಂಖ್ಯೆ	001–25–000019
ಕರಾರು ಒಪ್ಪಂದ ಪತ್ರದ ಸಂಖ್ಯೆ ಮತ್ತು ದಿನಾಂಕ	EE/YNK/KPPP-16/AG0/2025-26, dt:26/05/2025
ಕಾರ್ಯಾದೇಶ ಸಂಖ್ಯೆ ಮತ್ತು ದಿನಾಂಕ	BBMP/EE/YNK.D/KPPP-16/W.O/14/2025-26, dt:26/05/2025
ಕಾಮಗಾರಿ ಒಟ್ಟು ಅಂದಾಜು ಮೊತ್ತ ರೂ.ಲಕ್ಷಗಳಲ್ಲಿ	50.00 Lakhs
ಪಿ–ಕೋಡ್	3861

****

ಮೇಲ್ಕಂಡ ವಿಷಯಕ್ಕೆ ಸಂಬಂಧಿಸಿದಂತೆ, ಕಾಮಗಾರಿಯ ಗುಣಮಟ್ಟವನ್ನು ದೃಢೀಕರಿಸುವ ಸಂಬಂಧ ಮಾನ್ಯ ಮುಖ್ಯ ಆಯುಕ್ತರು ರವರ ಕಛೇರಿ ಆದೇಶದ ಸಂಖ್ಯೆ:ಮು.ಆ/ಬಿ.ಬಿ.ಎಂ.ಪಿ/ಪಿ.ಆರ್/ ಜಿ/2383/2022–23, ದಿನಾಂಕ14–9–2022 ರಲ್ಲಿ ರೂ. 50.00 ಲಕ್ಷಗಳವರೆಗಿನ ಕಾಮಗಾರಿಗಳ ಗುಣಭರವಸೆಗೆ ಸಂಬಂಧಪಟ್ಟಂತೆ ವಿಭಾಗೀಯ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು ಸಂಪೂರ್ಣವಾಗಿ ಜವಾಬ್ದಾರರಾಗಿರುತ್ತಾರೆ ಎಂದು ಆದೇಶಿಸಿರುವ ಹಿನ್ನಲೆಯಲ್ಲಿ ಗುಣನಿಯಂತ್ರಣ ವಿಭಾಗದಿಂದ ಪರಿಶೀಲನೆಗೆ ಒಳಪಡಿಸಿರುವುದಿಲ್ಲ. ಆದರೆ ಸದರಿ ಕಾಮಗಾರಿಯ ಗುಣಮಟ್ಟವನ್ನು ಎನ್.ಎ.ಬಿ.ಎಲ್. ಯಿಂದ ಮಾನ್ಯತೆ ಪಡೆದ ಪ್ರಯೋಗಾಲಯವಾದ CIVIL AIM Consultants & Engineers. ಇವರು ಗುಣಮಟ್ಟ ಪರೀಕ್ಷೆ ಮಾಡಿ ಗುಣ ಮಟ್ಟವನ್ನು ಖಾತ್ರಿಪಡಿಸಿರುವುದರಿಂದ ಗುಣಭರವಸೆ ವಿಭಾಗದ ವತಿಯಿಂದ ಗುಣಮಟ್ಟದ ಬಗ್ಗೆ ಅಭಿಪ್ರಾಯ ಪಡೆದಿಲ್ಲದಿರುವುದಾಗಿ ದೃಢೀಕರಿಸಿದೆ.

ಸಹಾಯಕ ಅಭಿಯಂತರರು
ವಾರ್ಡ್ ನಂ:01

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಯಲಹಂಕ ಉಪವಿಭಾಗ
ಬಿಬಿವರಪ ಬೆಂಗಳೂರು–560064

Asst. Executive Engineer
Yelahanka Sub Division
(BBMP Ynk. Zn)
Yelahanka, Bangalore

ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು,
ಯಲಹಂಕ ವಿಭಾಗ, ಬಿಎಂಪಿ, ಬೆಂಗಳೂರು–64

ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ

ಯಲಹಂಕ ಉಪವಿಭಾಗ, ಬೆಂಗಳೂರು.

ಚೆಕ್ ಲಿಸ್ಟ್

ಸ.ಕ್ರ.	ವಿವರಗಳು	
1	ಕಾಮಗಾರಿಯ ಹೆಸರು	Resurfacing of roads at Maruthinagara 3rd Main, 6th, 7th and 8th cross roads in Kempegowda ward no:01
2	ಅಂದಾಜು ಮೊತ್ತ ರೂ.ಲಕ್ಷಗಳಲ್ಲಿ	Rs.50.00 lakhs
3	ಪರಿಷ್ಕೃತ ಟೆಂಡರ್ ಮೊತ್ತ	NA
4	ಕಾಮಗಾರಿ ಆಯವ್ಯಯದಲ್ಲಿ ಸೇರ್ಪಡೆಯಾಗಿದೆಯೇ?	NA
5	ತಾಂತ್ರಿಕ ಮಂಜೂರಾತಿ ಸಂಖ್ಯೆ	BBMP/EE/YZ/TS/167/2024-25 07/3/2025
6	ಆಡಳಿತಾತ್ಮಕ ಅನುಮೋದನೆ ಸಂಖ್ಯೆ	BBMP/EE/ZD/AS/55/2024-25 07/3/2025
7	ಈ ಕಾಮಗಾರಿಯ ಈ ಹಿಂದಿನ ಕೌನ್ಸಿಲ್ ಅನುಮೋದನೆ ಗೊಂಡಿರುವ ದೃಢೀಕರಣ ಪತ್ರದ ನಕಲು	NA
8	ಕಾಮಗಾರಿಯು ಪಾರದರ್ಶಕ ನಿಯಮ 2000 ಹಾಗೂ ಸಂಬಂಧಿಸಿದ ಆದೇಶ ಸುತ್ತೋಲೆಯಂತೆ ನಿರ್ವಹಿಸಲಾಗಿದೆಯ?	Yes
9	ಕಾಮಗಾರಿಯನ್ನು ಕಾರ್ಯಗತ ಮಾಡಿರುವ ವಿಧಾನ	Tender
10	ಗುತ್ತಿಗೆದಾರರ ಹೆಸರು	Sri.Vinayaka Enterprises Prop.B.R.Mohan
11	ಕಾಮಗಾರಿಯಬಿಲ್ಲಿನ ಮೊತ್ತ ತಾಂತ್ರಿಕ ಮಂಜೂರಾತಿ ಹಾಗೂ ಆಡಳಿತಾತ್ಮಕ ಮಂಜೂರಾತಿ ಮೊತ್ತದ ಮಿತಿಯಲ್ಲಿ ಇದೆಯೇ?	Yes

ಸಹಾಯಕ ಅಭಿಯಂತರರು,

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು,
ಯಲಹಂಕ ಉಪವಿಭಾಗ,
ಬಿ.ಬಿ.ಎಂ.ಪಿ, ಬೆಂಗಳೂರು-560064.

Yelahanka, Bangalore

ಕಛೇರಿ ಪರಿಶೀಲನೆ

ಕಾಮಗಾರಿಯ ಬಿಲ್ಲನ್ನು ಪರಿಶೀಲಿಸಿರುತ್ತೆ. ಇದರ ಮೊತ್ತ ರೂ 43,52,601 ಗಳು ಗುತ್ತಿಗೆದಾರರಾದ B.R.MOHAN ರವರಿಗೆ ಪಾವತಿ ಮಾಡಲು ಲೆಕ್ಕ ಶಾಖೆಗೆ ಕಡತವನ್ನು ರವಾನಿಸಿದೆ.

ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು,
ಯಲಹಂಕ ವಿಭಾಗ,
ಬಿ.ಬಿ.ಎಂ.ಪಿ, ಬೆಂಗಳೂರು.

Bruhath Bengaluru Mahanagara Palike.

Yalahanka Sub Division, Bangalore-560064

Completion Report

Work Record No

Name of work:-	Resurfacing of roads at Maruthinagara 3rd Main, 6th, 7th and 8th cross roads in Kempegowda ward no:01			
1) Sanctioned Estimate No. and Date :	CE/TS/~~22~~/167/07/03/2025			
2) Name of Contractor	Sri.Vinayaka Enterprises Prop.B.R.Mohan			
3) Time stipulated for completion of work	90 days			
4) Date of Commencement of Work	26/05/2025			
5) Date of Completion of Work	31/07/2025			
M B No	1304/2024-25			
Page No	130361 to 130365.			
6) Name of the officer official incharge of the work				
1) Asst. Exe. Engineer	Sri Raghunandan Mantri.			
2) Asst. Engineer	Sri. G. prakash			
Estimate Amount / Tender	Amount claimed asper actuals	Excess	Savings	Remarks
50 lakhs	5144330:00	—	—	—

1 **Certified that the above work has been completed with in the stipulated time Sinoted in entrustment**

2 **Certified that above work has been executed satisfactorily**

AE, Ward No :01

Asst.Executive Engineer
Yelahanka Sub Division
BBMP, Bangalore

Executive Engineer
Yelahanka Division
BBMP, Bangalore

Resurfacing of roads at Maruthinagara 3rd Main, 6th, 7th and 8th cross roads in Kempegowda ward no:01 ನಾಮಾಂಕಿತದ ಕಾಮಗಾರಿಯ ಬಿಲ್ಲಿಗೆ ಸಂಬಂಧಿಸಿದಂತೆ ಕೆಳಕಂಡ ಅಂಶಗಳುಳ್ಳ ಮಾಹಿತಿ / ವಿವರಗಳೊಂದಿಗೆ ಎಲ್ಲಾ ಅಗತ್ಯ ದಾಖಲೆಗಳನ್ನು ಪರಿಶೀಲಿಸಿ ಆನ್ ಲೈನ್ ನಲ್ಲಿ ಅಪ್ ಲೋಡ್ ಮಾಡಲಾಗಿದೆ.

ಕ್ರ.ಸಂ	ಕಡತದಲ್ಲಿ ಪರಿಶೀಲಿಸಬೇಕಿರುವ ದಾಖಲೆಗಳು/ ಮಾಹಿತಿಗಳ ವಿವರ	ಕಡತದಲ್ಲಿನ ದಾಖಲೆಗಳು/ಮಾಹಿತಿಗಳು ಲಭ್ಯವಿರುವ ವಿವರ
1	ಮೂಲ ಜಾಬ್ ಕೋಡ್ ಪ್ರಮಾಣ ಪತ್ರ / Oruginal Jobcode	001.25-000019
2	ಬಿಲ್ಲಿನ ಎಲ್ಲಾ ದಾಖಲಾತಿಗಳಲ್ಲಿನ ಕಾಮಗಾರಿಯ ನಾಮಾಂಕಿತವು ಮೂಲ ಜಾಬ್ ಕೋಡ್ ನಾಮಾಂಕಿತದಂತೆ ಇರುವ ಬಗ್ಗೆ / Name of work should tally in all documents as per Original Jobcode	Yes
3	ಅಂದಾಜುಪಟ್ಟಿ (ಅಭಿಯಂತರರ ಸಹಿ ಮತ್ತು ಮೊಹರುಗಳು) / Approved estimate with AS/TS seal	
4	ಅಂದಾಜುಪಟ್ಟಿ ನಕ್ಷೆ /ಅಳತೆ ಪುಸ್ತಕದ ನಕ್ಷೆ ಒಂದೇಯಾಗಿರುವ ಬಗ್ಗೆ / Sketch should be same in both estimate and MB	
5	ಆಡಳಿತಾತ್ಮಕ ಮೆಮೋ ಪ್ರತಿ ಮತ್ತು ದಿನಾಂಕ / Approved AS Memo and date	
6	ತಾಂತ್ರಿಕ ಮೆಮೋ ಪ್ರತಿ ಮತ್ತು ದಿನಾಂಕ / Approved TS Memo and date	
7	ಡಿಟಿಎಸ್ ಅನುಮೋದನೆ ಪ್ರತಿ / Approved DTS copy	
8	ಟೆಂಡರ್ ನೋಟಿಫೀಕೇಶನ್, ಪ್ರತ್ರಿಕಾ ಪ್ರಕಟಣೆ, ಜಿಲ್ಲ ಬುಲೆಟಿನ್ ಪ್ರತಿಗಳು / Tender Notification , Paper cutting and state or district bulletine copies	Enclosed.
9	ಆನ್ ಲೈನ್ ಟೆಂಡರ್ ಅನುಮೋದನೆ ಪ್ರತಿ / Online Tender approval copy	
10	ಎಲ್.ಓ.ಎ ಮತ್ತು ಪಿ.ಎಸ್.ಡಿ / LOA and PSD	
11	ಕರಾರು ಒಪ್ಪಂದದ ಪ್ರತಿ / Agreement Copy	
12	ಕಾರ್ಯಾದೇಶ / Work order	
13	ಷೆಡ್ಯೂಲ್-ಬಿ / Schedule B	
14	ಜಿಯೋ ಟ್ಯಾಗ್ ಛಾಯಾಚಿತ್ರಗಳು / Geo Tag Photos	
15	ಆನ್ ಲೈನ್ ರಸ್ತೆ ವಹಿ / Approved Online Road History	
16	Standard Tender Documents	
17	I. Measurement Book/E-MB Shall have	
	Following:-	
	Name of the work	

	Work order No and date	W.O | 14 | 25-26 dt. 26 | 05 | 25
	Date of Pre-measurements / Measurements (RA/Final etc... as the case may be but the dates shuld be After Work order)	
	should be After work order Date	
	Item Wise Measurement (as per standard recording requirements)	
	Check Measurement with date / dates by the concerned AEE / EE as per codal requirements	
	Completion certificate as the case may be.	
	Sketch recorded in the measurement book (for Items /works executed)- tallies which sketches as per original Sanctioned estimate	Varified.
	In case of final Bills / Claims, the agency shall accept in writing as per codal Procedure	
	Divisional accounts officials shall check and verify the arithmetical calculation as required under A code.	
18	I. In case of deviation of the quanities Work slip / EIRL during execution:-	
	For deviation in quantity deviation carried out / executed over and above sanction BOQ	
	Chief Engineer Inspection report	
	Approval of Work Slip (PWG-4S-A code-II)	
	Approval of EIRL (PWG-195, D Code-I)	
	Acceptance letter by agency to carry out additional items	Not Applicable.
	Supplementary agreement { (D Code-I) (195 (8) (9) (10) }	
19	II Depending on the quantities variations and amount modified / revised estimate with Adminstrative Approval and Technical sanction details as the case may be.	
	Name of the work	
	Work order No and date	
	Date of Measurements Recorded (including Pre-measurements)	
	Check measurement date by AEE	
	Acceptance Signature of Agency	021 | 31-07-25
	SBR No with date	

	B.R No with date	
	Quantity of recorded items in contract certificate shall tally with the measurement book and BOQ	Yes.
	Statutory deductions as per prevailing norms code.	deducted.
20	**IV. Other details:-**	
	Completion certificates duly certified by the competent authority in case of final bills { (D Code-) 185(d)) {(Form PWG-46- A code-II))	E.E. certified
	Penalty in case of delay in completion of works.	NA
	E 0 T (Extension of Time) — Accorded if any as per norms.	
	Price Adjustment (if the clause included in the tender)	
	Quality Assurance test reports as per MORT & H or other relevant standards. (No of tests reports / results should be on par with the frequency as stipulated in MORT&H or other relevant standards)	Yes

Account Superintendent,
Yelahanka Divisioin,
BBMP, Bangalore-64

YNK-DBR No.....
Date.....

ಸ.ಕಾ.ಅ/ಯ೦.ಉ.ವಿ.
ಎಸ್.ಬಿ.ಆರ್. ಸಂಖ್ಯೆ: 021
ದಿನಾಂಕ: 31-7-2025

Original / Duplicate / Triplicate

No. 1st & final bill

CONTRACT CERTIFICATE

(For Other Works)

Date.....

Division: Yelahanka Division
Bill Received No..... ...Dated.....Cash Book Voucher No.....dated.....
Scheduled Docket No.....
Sub Division: Yelahanka Division.

Name of Work - Resurfacing Of Roads At Maruthi Nagara 3rd Main 6th, 7th, and 8th Cross Roads in Kempegowda Ward No-01.

Job Code No:001-25-000019

Est. cost: 50.00 lakhs

Name of Contractor and Full Address : VINAYAKA ENTERPRISES, Prop B.R MOHAN
Work Order No:**BBMP/EE/YNK.D/KPPP-16/W.O/14/2025-26**

Dated : 26-05-2025

Certified that the measurements were taken by me on 31/7/2025 and recorded in pages 130361 to 130365 of measurement Book No.....1304..... and that the work is satisfactorily executed.

Contractor

Officer-in-charge of work

Certified that the measurements were taken by me on..... and found correct. The work is satisfactorily executed.

Certified that the quantities of materials shown in column 3 of Account II have been actually brought to site of the work and the contractor has not previously received any advance on this security. These materials are of an imperishable nature and are all required for immediate use on the work in connection with items for finished work have been agreed upon. A normal agreement signed and executed by the contractor is recorded in the office.

Sub-Division Officer

Asst. Engineer
Yelahanka Division
(BBMP Yelahanka)
Yelahanka, Bangalore

If Memorandum of Payment

1) Total value of work done or supplies made as per account within → 4359601
2) Deduct amount to be held in reserve being.....percent Rs..... → GST 784728
3) Deduct amount to be held in Balance → 4.T 5144330
4) Deduct Payment :
   a) Amount of previous payment as in the Office Cash Book Voucher No.....Dated.....S.D No.....
   Amount adjusted towards cash advance recovery of → PSD 217980
   b) Payments cost store or other materials supplied. → LT 43596
   Now made recovery of amount creditable to this/other work → LC 43596
   Amount paid on this bill Cheque/Cash → LGST 43596
5) Balance being unpaid value of work done held in reserve → SGST 43596
6) Deduct cash advance made on the office Cash Book Voucher No..... → CBF 4360
   date .....less adjustments → LR 47560
7) Net amount due to or from contractor → T.D 444284
Unadjusted items → Net 4700046
8) Advance to contractor for materials brought to site (as detailed) within value of Governme
   materials supplied

Contractor's Signature

Received Rs.....(in words)
By Cash and by adjustment of Payment as per memorandum.

(For use in the Office)

Audited & Admitted for Rs. 5144330=00
4700046=00 by Cheque
and Rs. 444284=00 by adjusement

Witnesses :

1.

2.

Dated.....Signature of Contractor

Paid by me by cheque No.....Dated.....

Cash Rs.....Dated.....

Accts. Supdt.
Yelahanka Division
BBMP

Executive Engineer

Exe. Engineer
Yelahanka Division
BBMP

Initials of Officer Making Payment

Name of Work-"Resurfacing Of Roads At Maruthi Nagara 3rd Main 6th, 7th, and 8th Cross Roads in Kempegowda Ward No-01

ABSTRACT

Sl No	Description of Work	Unit	As per Shedule -B			Previous measurement		Present Measurement			Up to date	
			Qty	Rate	Amount	Qty	Amount	Qty	Rate	Amount	Qty	Amount
1	Removing And Resetting Of Footpath Slab [Approved Rate]	Sqm	434.52	242.03	105166.88	-	-	434.52	242.03	105166.88	434.52	105166.88
2	Earth work excavation by manual means for drains,canals, waste weir, draft, approach channels, key trenches, foundation of bridges and such simillar works in all kinds of soils , as per drawing and technical specifications, including setting out, shoring, strutting, barricading, caution lights, removal of stumps and other deleterious matter, excavated surface leveled and sides neatly dressed disposing off the excavated stuff or sorting & stacking the selected stuff for reuse in a radius of 50 m and lift upto 1.5 m including cost of labour, tools & other appurtenaces required to complete the work . Loading and Unloading of Stone Boulder/Stone aggregates/Sand/Kankar/Moorum.(Tipper 14 m3) complete as per the direction of Engineer In charge of the work	Cum	449.57	371.59	167057.48	-	-	449.49	371.59	167025.99	449.49	167025.99
3	Providing and laying in position plain cement concrete for levelling course for all works in foundation. The granite/trap/basalt crushed graded coarse aggregates and fine aggregates as per relevant IS Codes machine mixed, laid in layers not exceeding 150 mm thickness, well compacted using plate vibrators, including all lead & lifts, cost of all materials of quality, labour, Usage charges of machineries, curing, and all the other appurtenances required to complete the work as per technical specifications. (The cost of steel reinforcement & formwork shall be paid separately) Mix 1:3:6 (M10) Using 40 mm nominal size graded crushed coarse aggregates complete as per the direction of Engineer In charge of the work	Cum	31.80	6784.88	215759.18	-	-	31.77	6784.88	215555.64	31.77	215555.64
4	Supplying, Fitting and Placing un-coated TMT bar Reinforcement in sub-structure complete as per Drawing and Technical Specifications.complete as per the direction of Engineer In charge of the work	Tn	3.72	89510.77	333033.77			3.72	89510.77	332980.06	3.72	332980.06

Sl No	Description of Work	Unit	As per Shedule -B			Previous measurement		Present Measurement			Up to date	
5	Providing and laying in position Reinforced cement concrete for all Sub structures of building, Irrigation works, Sub structure works of bridges, Drain works & other parallel works from 0.50m to 3.50 m height. The granite/trap/basalt crushed graded coarse aggregates and fine aggregates as per relevant IS Codes machine mixed with super plasticisers, laid in layers, well compacted using needle vibrators, providing weep holes wherever necesary, including all lead & lifts, cost of all materials of quality, confirming to the requirements of relevant IS codes, labour, Usage charges of machinery, curing and all other appurtenances required to complete the work as per technical specifications. (The cost of steel reinforcement & formwork to be paid separately) M20 Design Mix Using 20 mm nominal size graded crushed coarse aggregates complete as per the direction of Engineer In charge of the work	Cum	90.84	9670.41	878460.04	-	-	90.82	9670.41	878266.64	90.82	878266.64
6	Providing and fixing precast reinforced cement concrete covering slabs of 10Cm thick made of M20 with OPC cement, with 20mm and down size graded granite metal coarse aggregate @0.70cum and fine aggregate & 0.74 cum with superplasticizer machine,mixed, Inculding providing and removing centering, shuttering, strutting propping etc., for edges of slabs with TMT steel (Fe500) cost of all materials, labour, all lead and lift, HOM of machinery, curing, including cost of reinforcement etc., complete as directed by the Engineer in charge of the work	Sqm	267.63	2133.95	571109.04	-	-	267.57	2133.95	570981.00	267.57	570981.00
7	Earth work in surface excavation by mechanical means for lowering & leveling the ground for all works other than foundation in all kinds of soils & upto depth not exceeding 300mm as per drawing and technical specifications, including setting out, shoring, strutting, barricading, caution lights, removal of stumps and other deleterious matter including dressing of excavated surfaces, disposing off or levelling the excavated earth or sorting & stacking the selected earth for reuse in a radius of 50 m and lift upto 1.5 m including cost of labour, tools, usage of machinery & other appurtenances required to complete the workcomplete as per the direction of Engineer In charge of the work	Cum	92.53	107.62	9958.08			92.52	107.62	9957.00	92.52	9957.00

Sl No	Description of Work	Unit	As per Shedule -B			Previous measurement		Present Measurement			Up to date	
8	Providing, laying, spreading and compacting graded stone aggregate to wet mix macadam specification including premixing the Material with water at OMC in mechanical mix plant carriage of mixed Material by tipper to site, laying in uniform layers with paver/grader in sub-base /	Cum	104.10	2899.07	301782.32	-	-	104.09	2899.07	301764.20	104.09	301764.20

Sl No	Description of Work	Unit	As per Shedule -B			Previous measurement		Present Measurement			Up to date	
8	Providing, laying, spreading and compacting graded stone aggregate to wet mix macadam specification including premixing the Material with water at OMC in mechanical mix plant carriage of mixed Material by tipper to site, laying in uniform layers with paver/grader in sub-base / base course on well prepared surface and compacting with vibratory roller to achieve the desired density complete as per the direction of Engineer In charge of the work	Cum	104.10	2899.07	301782.32	–	–	104.09	2899.07	301764.20	104.09	301764.20
9	Providing and applying primer coat with SS1 grade Bitumen Emulsion on prepared surface of granular base including cleaning of road surface and spraying primer at the rate of 0.90 kg per m2 using mechanical means. complete as per the direction of Engineer In charge of the work	Sqm	462.65	46.45	21490.09	–	–	462.62	46.45	21488.70	462.62	21488.70
10	Providing and applying tack coat with VG-10 Bitumen using pressure distributor at the rate of 0.20 kg/m2on the prepared bituminous surface cleaned with mechanical broom complete as per the direction of Engineer In charge of the work	Sqm	2532.50	13.59	34416.68	–	–	2532.33	13.59	34414.36	2532.33	34414.36
11	Providing and laying Dense Graded Bituminous Macadam with 40/60 TPH capacity HMP using crushed aggregates of specified grading, premixed with bituminous binder VG-30, @ 4.5 per cent by weight of total mix and filler, transporting the hot mix to work site, laying with mechanical paver finisher to the required grade, level and alignment, rolling with smooth wheeled, vibratory and tandem rollers to achieve the desired compaction as per MoRTH specification clause No. 505 complete in all respects. complete as per the direction of Engineer In charge of the work	Cum	30.98	10704.68	331630.99	–	–	30.96	10704.68	331416.89	30.96	331416.89
12	Providing and laying Bituminous Concrete with 40/60 TPH capacity hot mix plant using crushed aggregates of specified grading, premixed with bituminous binder VG-30, @ 5.4 per cent of mix and filler, transporting the hot mix to work site, laying with mechanical paver finisher to the required grade, level and alignment, rolling with smooth wheeled, vibratory and tandem rollers to achieve the desired compaction as per MORTH specification clause No. 507 complete in all respectscomplete as per the direction of Engineer In charge of the work	Cum	101.30	12409.68	1257100.58			101.29	12409.68	1256976.49	101.29	1256976.49
13	Providing and laying of hot applied thermoplastic compound 2.5 mm thick including reflectorising glass beads @ 250 g/ m2 area, thickness of 2.5 mm is exclusive of surface applied glass beads as per IRC:35:2015.The finished surface to be level, uniform and free from streaks and holescomplete as per the direction of Engineer In charge of the work	Sqm	120.70	600.43	72471.90	–	–	117.80	600.43	70730.65	117.80	70730.65

Sl No	Description of Work	Unit	As per Shedule -B			Previous measurement		Present Measurement			Up to date	
14	Cost of Haulage Excluding Loading and Unloading Taking output 25 t load and lead 10 km = 100 t.km complete as per the direction of Engineer In charge of the work	T.km	693.89	90.63	62887.62			693.78	90.63	62877.28	693.78	62877.28
	SUB TOTAL				4362324.00					4359601.78		4359601.78
	GST 18%				785218.00					784728.32		784728.32
	GRAND TOTAL				5147542.00					5144330.10		5144330.10

CERTIFICATE

1 Certified that the work done is satisfactorily.

2 There is no departmental issues by BBMP

Contractor

Assistant Engineer

Asst. Executive Engineer

Asst. E... Engineer
Yela... Division
(BBMP Mtk. Zn)
Yelahanka, Bangalore

No. 1st & final

Division: Yelah...
Bill Received ...
Scheduled Doc...
Name of Wor...

Job Code N...
Name of Co...
Work Orde...

Certified th...
of measure...

Contrac...

Certified ...

Certifie...
the cond...
are all ...
agreem...

If Me...

ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ
Bruhat Bangalore Mahanagara Palike

BBMP ENGINEERING DEPARTMENT

Road History Data Sheet

1.General Details

Zone No:Yelahanka **Ward No:1** **Ward Name:Kempegowda Ward**

Street ID: W0152,W0154 **Street Name:**

Significant Landmark: Maruthinagara Third Main Eighth Cross and Seventh Cross

Segment_No: 1/S-W0154/S14946 **Total_Length: 555.76**

Segment Details

Seg No.	Length(mts)	Start Coordinates	End Coordinates	From Landmark	To Landmark	Work Type	Other Work
4	138.8	13.109456322031357.609868049621	13.109490282016749-77.608604729175	Maruthinagara 3rd Main 8th Cross	Maruthinagara 3rd Main 8th Cross	Asphalting	Asphalting
1	139.08	13.109163743501433-77.609921693801	13.109197703527212-77.608650326728	Maruthinagara 3rd Main 7th Cross	Maruthinagara 3rd Main 7th Cross	Asphalting	Drain and Asphalting

2.Work Details

History of Road / Lane / Circles

Name of the Work:Resurfacing of roads at Maruthinagara 3rd main 6th 7th and 8th cross roads in Kempegowda ward No:01

Sanctioned Amount: 5000000 **Sanctioned Year: 2024-25** **Year: 2025-26**

Tender: Tender **Work Details: Resurfacing of roads at Maruthinagara 3rd main 6th 7th and 8th cross roads in Kempegowda ward No:01** **Job No/Work Code:001-25-000019**

Work Order No: BBMP/EE/YNK-D/EPMT-16/WO-14/2025-26 **Work Order Date: 26/05/2025** **Period of Extention: 0**

Defect Liability Period From: 31/07/2025 **Defect Liability Period To: 30/07/2026**

3.Contractor Details

Zone: Yelahanka **Ward No: 1** **Ward Name: Kempegowda Ward**

Street ID: W0154 **Name of Contractor: VINAYAKAENTERPRISESProBRMOHAN** **Contractor Reg No (BBMP/PWD): CBSC1CIVIL188002024**

4.Field Inspection Details

Category	Image
Resurfacing of roads at Maruthinagara 3rd main 6th 7th and 8th cross roads in Kempegowda ward No:01	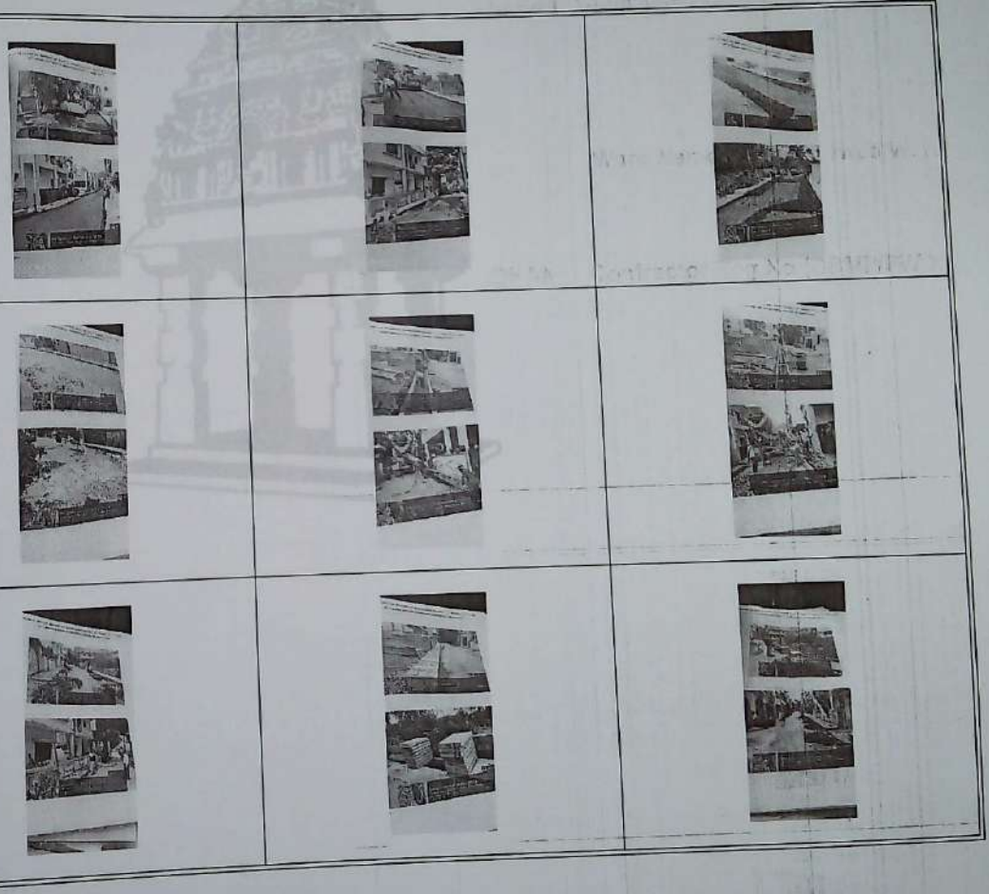

Remarks

Sl.No	Stage_No	Designation	Remarks	StageName	Action	Date
1	1	AE	Road Work History Added	Data Uploading	Initated	31-07-25
2	2	AEE	Approved	Review Application	Approved	31-07-25

3	3	EE	Approved	Review Application	Approved	31-07-25
4	4	SE	Forwarded For Approval as Recommended by EE	Review Application	Approved	31-07-25
5	5	CE	As proposed	Final Approval	Approved	31-07-25

RESURFACING OF ROADS AT MARUTHINAGARA 3rd MAIN 6th, 7th AND 8th CROSS ROADS IN KEMPEGOWDA WARD NO-01

GPS Map Camera
Bengaluru, Karnataka, India
Shahana Manzil, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.109493° Long 77.609944°

GPS Map Camera
Bengaluru, Karnataka, India
128, 14th Cross Rd, Palahalli, Tirumanahalli, Bengaluru, Karnataka 560001, India
Lat 13.109526° Long 77.608527°

A.E

A.E.E.

RESURFACING OF ROADS AT MARUTHINAGARA 3rd MAIN 6th, 7th AND 8th CROSS ROADS IN KEMPEGOWDA WARD NO-01

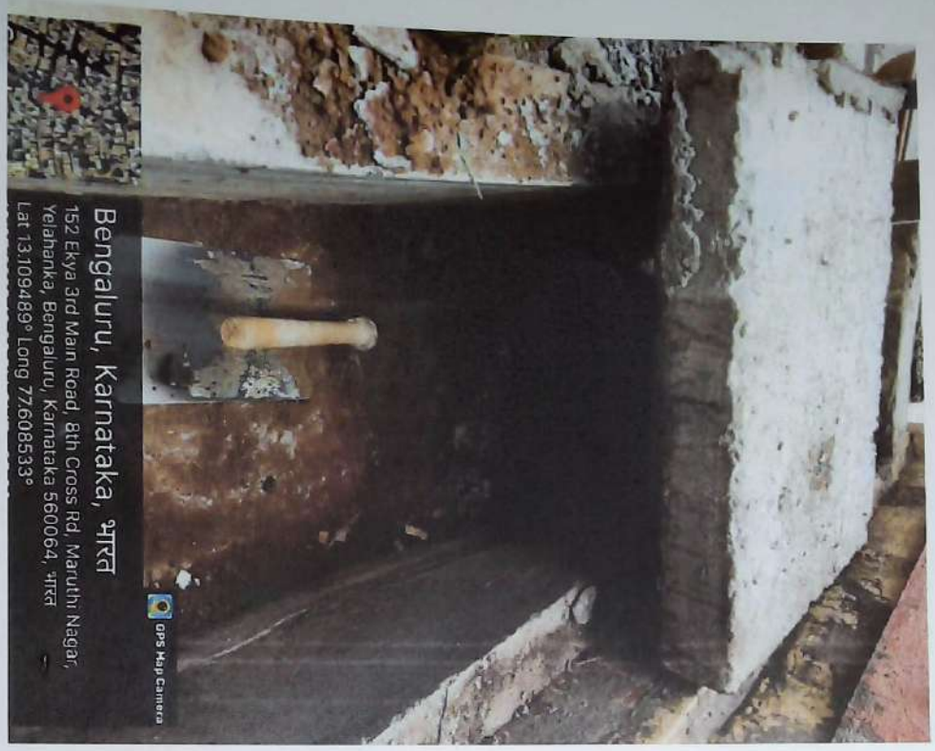
Bengaluru, Karnataka, भारत
152 Ekya 3rd Main Road, 8th Cross Rd, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, भारत
Lat 13.109489° Long 77.608533°
GPS Map Camera

Bengaluru, Karnataka, India
154, 14th Cross Rd, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.109452° Long 77.608751°
GPS Map Camera

A.E

A.E.E

RESURFACING OF ROADS AT MARUTHINAGARA 3rd MAIN 6th, 7th AND 8th CROSS ROADS IN KEMPEGOWDA WARD NO-01

GPS Map Camera
Bengaluru, Karnataka, India
214, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.109043° Long 77.609306°

GPS Map Camera
Bengaluru, Karnataka, India
163, 14th Cross Rd, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.109108° Long 77.609225°

A.E

A.E.E

RESURFACING OF ROADS AT MARUTHINAGARA 3rd MAIN 6th, 7th AND 8th CROSS ROADS IN KEMPEGOWDA WARD NO-01

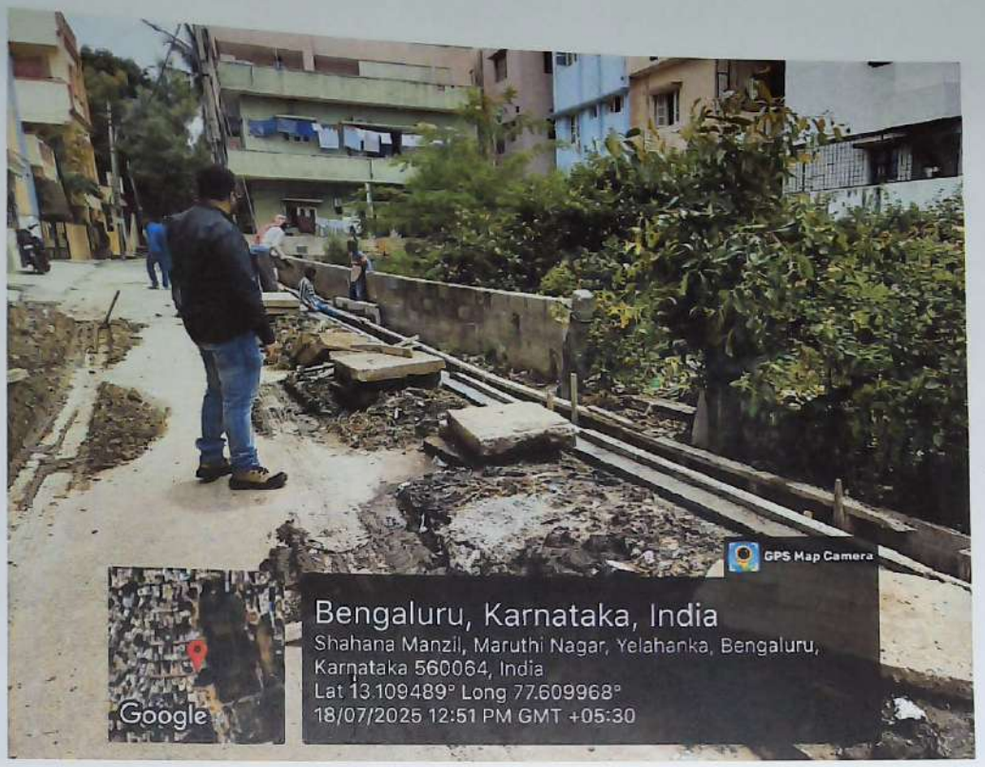
GPS Map Camera
Bengaluru, Karnataka, India
Shahana Manzil, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.109489° Long 77.609968°
18/07/2025 12:51 PM GMT +05:30
Google

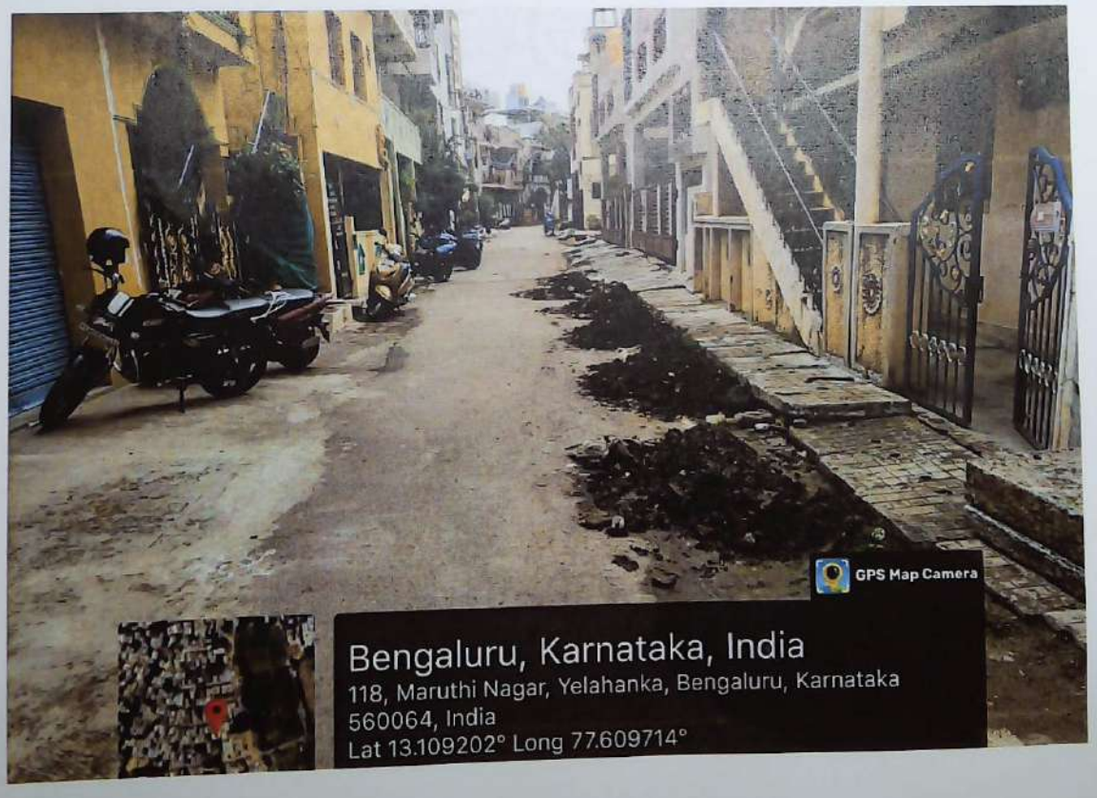
GPS Map Camera
Bengaluru, Karnataka, India
118, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.109202° Long 77.609714°

A.E

A.E.E.

RESURFACING OF ROADS AT MARUTHINAGARA 3rd MAIN 6th, 7th AND 8th CROSS ROADS IN KEMPEGOWDA WARD NO-01

GPS Map Camera
Bengaluru, Karnataka, India
No 152, Ekya, 3rd Main Road, 8th Cross Rd, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.109457° Long 77.608596°

GPS Map Camera
Bengaluru, Karnataka, India
156, 3rd Main Rd, Near Ashta Ganpathi Temple, Opposite Sri Mathru Krupa, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.109447° Long 77.608848°

A.E

A.E.E.

RESURFACING OF ROADS AT MARUTHINAGARA 3rd MAIN 6th, 7th AND 8th CROSS ROADS IN KEMPEGOWDA WARD NO-01

GPS Map Camera
Bengaluru, Karnataka, India
4j55+vwp, 3rd Main Rd, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.109484° Long 77.60976°
18/07/2025 12:52 PM GMT +05:30
Google

GPS Map Camera
Bengaluru, Karnataka, India
237, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.108833° Long 77.609343°

A.E

A.E.E

RESURFACING OF ROADS AT MARUTHINAGARA 3rd MAIN 6th, 7th AND 8th CROSS ROADS IN KEMPEGOWDA WARD NO-01

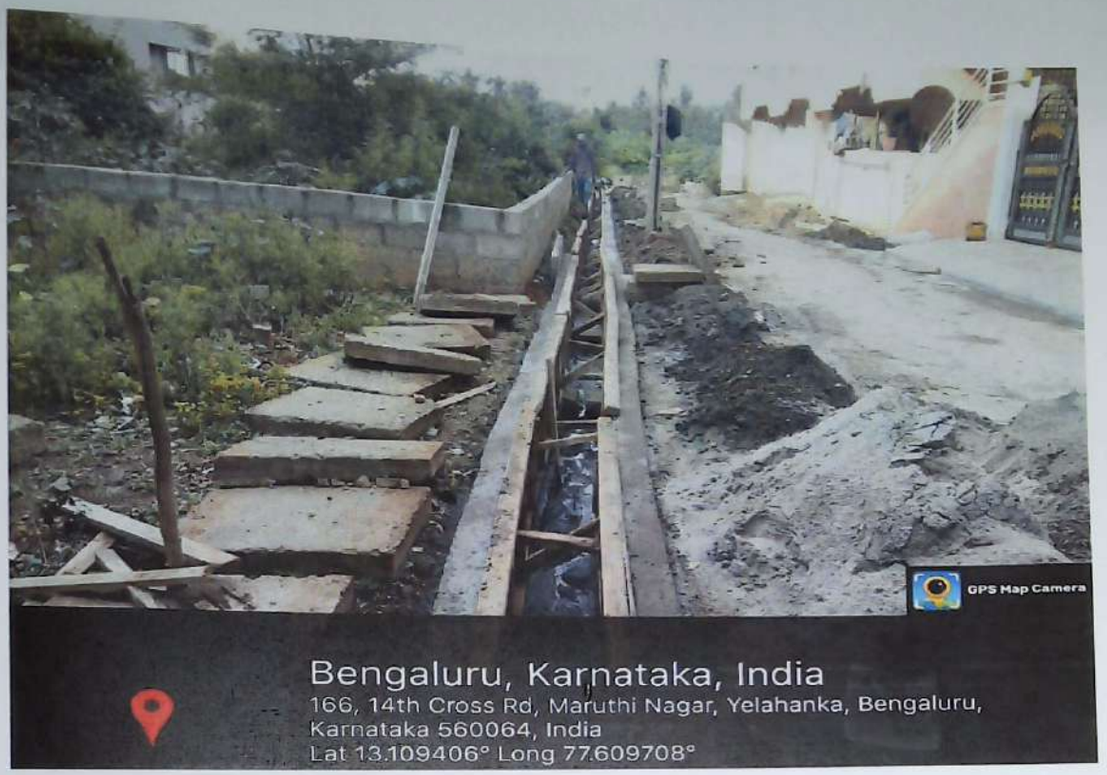
GPS Map Camera
Bengaluru, Karnataka, India
166, 14th Cross Rd, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.109406° Long 77.609708°

GPS Map Camera
Bengaluru, Karnataka, India
166, 14th Cross Rd, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.109446° Long 77.609824°

A.E

A.E.E

A.E.E.

RESURFACING OF ROADS AT MARUTHINAGARA 3rd MAIN 6th, 7th AND 8th CROSS ROADS IN KEMPEGOWDA WARD NO-01

GPS Map Camera
Bengaluru, Karnataka, India
4j55+ghq, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.109021° Long 77.609148°

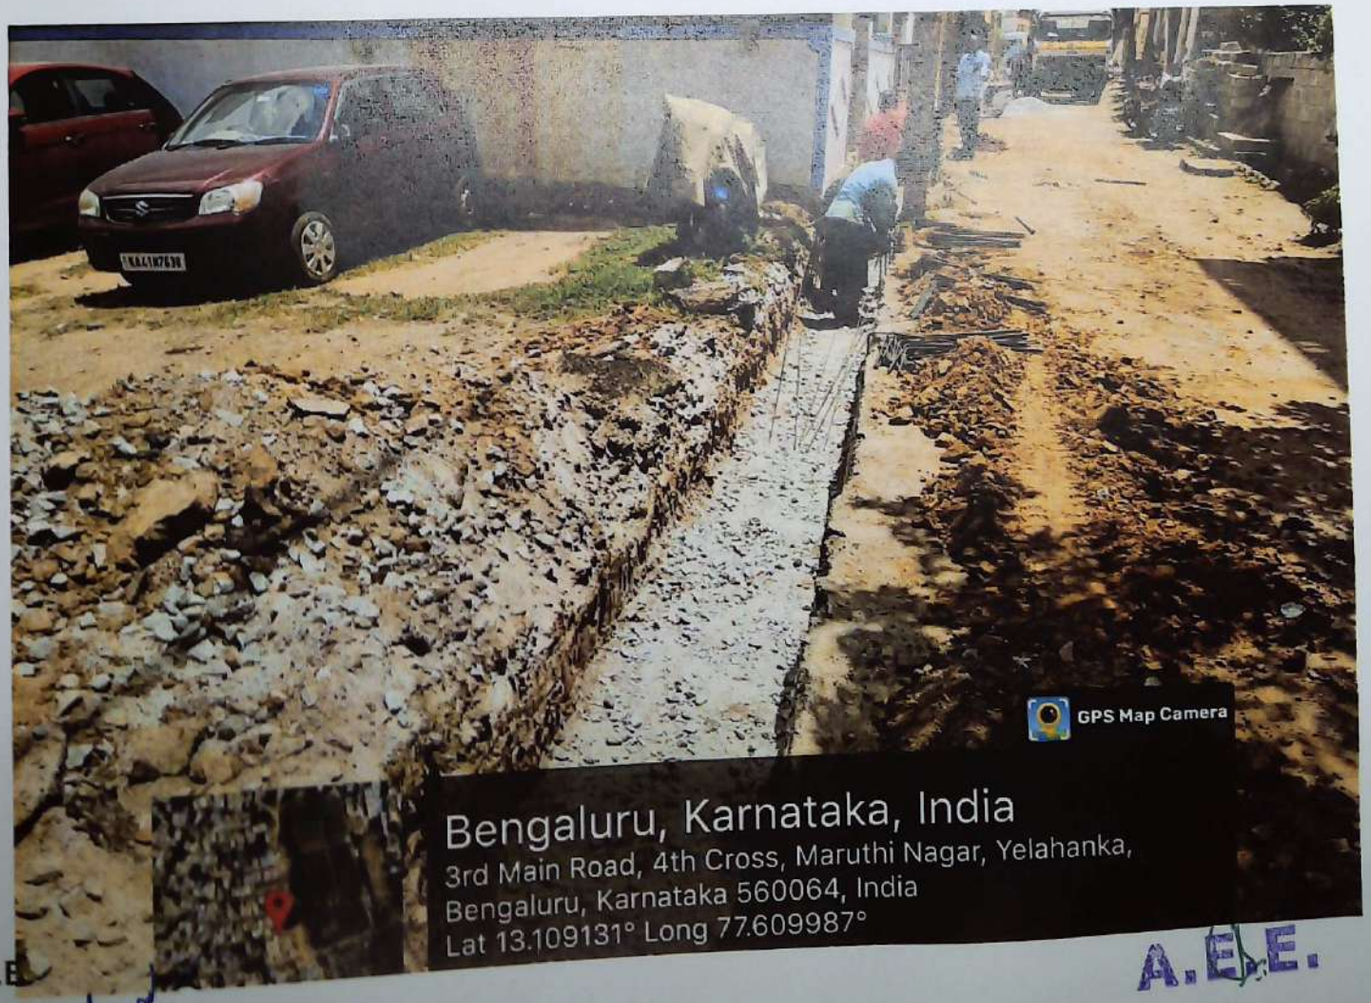
GPS Map Camera
Bengaluru, Karnataka, India
3rd Main Road, 4th Cross, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.109131° Long 77.609987°

A.E.

A.E.E.

RESURFACING OF ROADS AT MARUTHINAGARA 3rd MAIN 6th, 7th AND 8th CROSS ROADS IN KEMPEGOWDA WARD NO-01

GPS Map Camera
Bengaluru, Karnataka, India
211, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.109137° Long 77.609094°

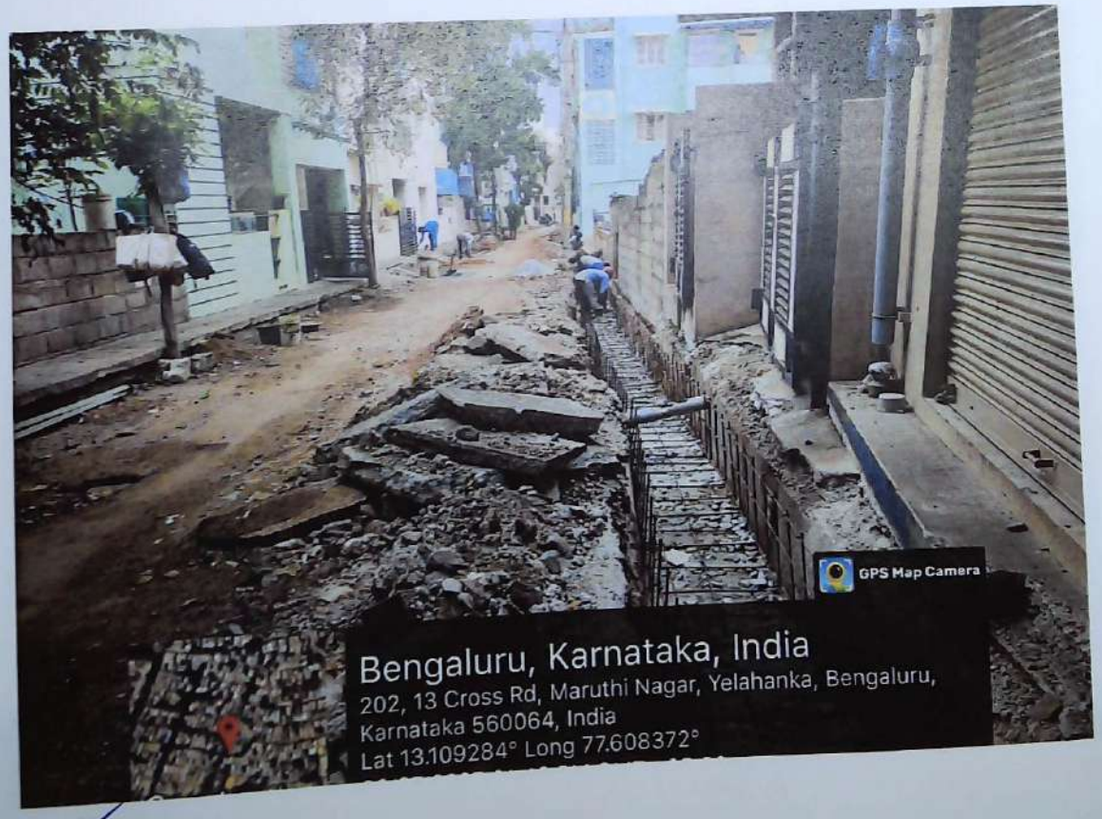
GPS Map Camera
Bengaluru, Karnataka, India
202, 13 Cross Rd, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.109284° Long 77.608372°

A.E.E

A.E

RESURFACING OF ROADS AT MARUTHINAGARA 3rd MAIN 6th, 7th AND 8th CROSS ROADS IN KEMPEGOWDA WARD NO-01

GPS Map Camera
Bengaluru, Karnataka, India
207, Palanahalli, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.109153° Long 77.608762°

A.E.E.

A.E

RESURFACING OF ROADS AT MARUTHINAGARA 3rd MAIN 6th, 7th AND 8th CROSS ROADS IN KEMPEGOWDA WARD NO-01

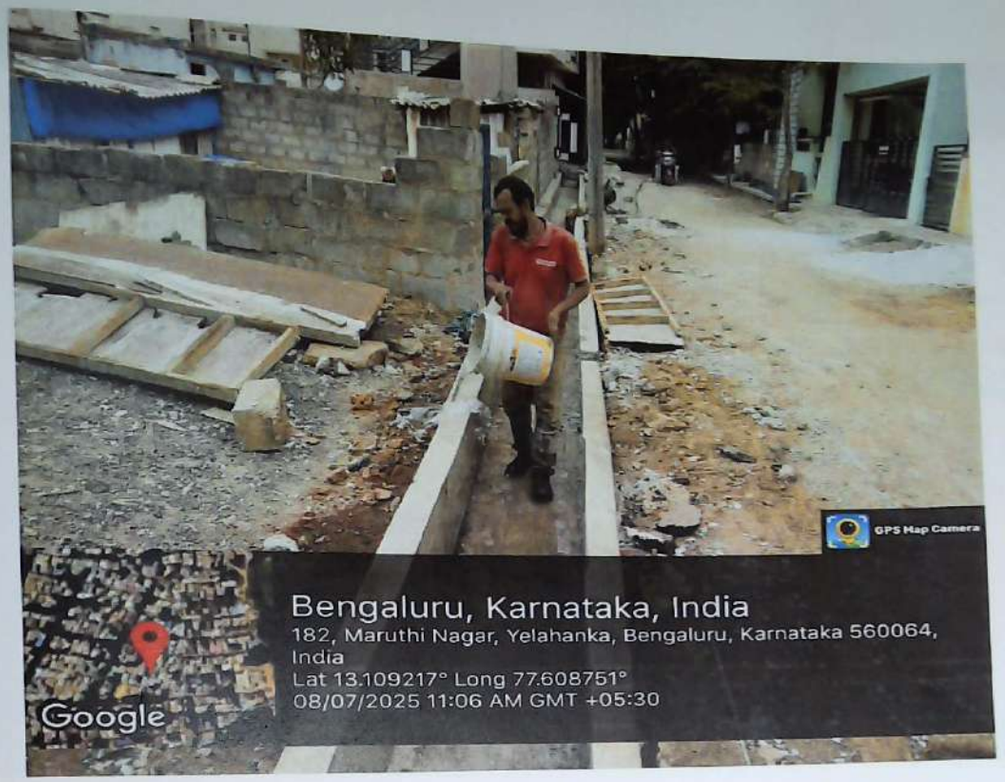
GPS Map Camera
Bengaluru, Karnataka, India
182, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.109217° Long 77.608751°
08/07/2025 11:06 AM GMT +05:30
Google

GPS Map Camera
Bengaluru, Karnataka, India
4j55+hvf, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.10892° Long 77.609783°

A.E.E.

A.E

RESURFACING OF ROADS AT MARUTHINAGARA 3rd MAIN 6th, 7th AND 8th CROSS ROADS IN KEMPEGOWDA WARD NO-01

GPS Map Camera
Bengaluru, Karnataka, India
207, Palanahalli, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.10923° Long 77.608759°

GPS Map Camera
Bengaluru, Karnataka, India
214, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.109124° Long 77.609263°

A.E

A.E.E.

RESURFACING OF ROADS AT MARUTHINAGARA 3rd MAIN 6th, 7th AND 8th CROSS ROADS IN KEMPEGOWDA WARD NO-01

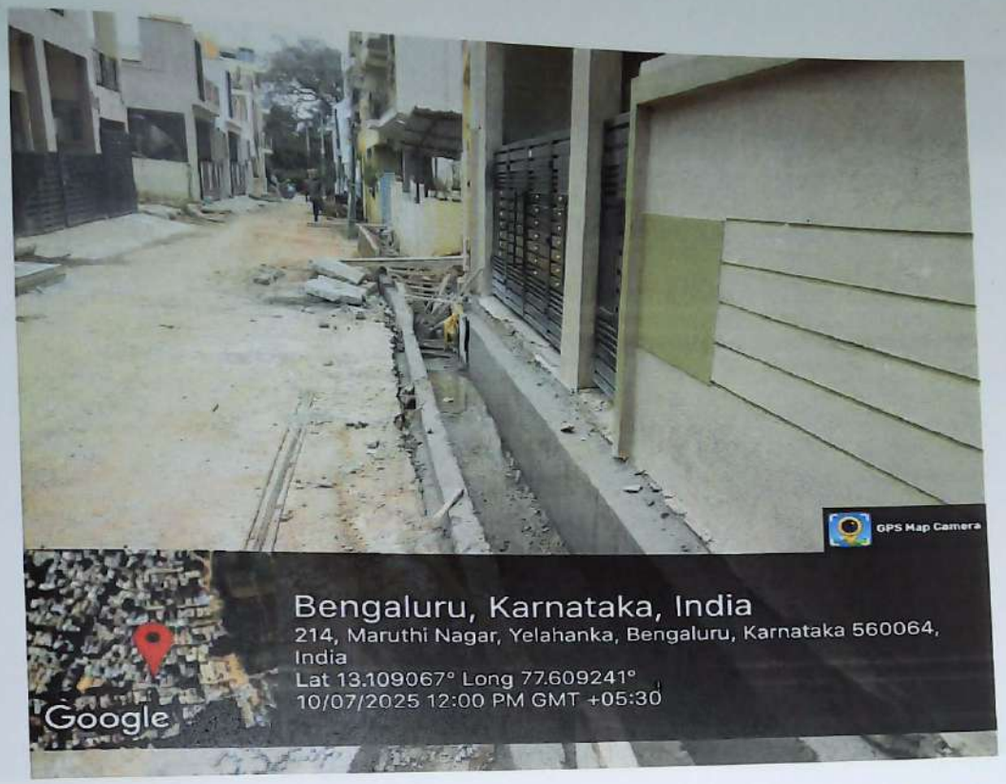
GPS Map Camera
Bengaluru, Karnataka, India
214, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.109067° Long 77.609241°
10/07/2025 12:00 PM GMT +05:30
Google

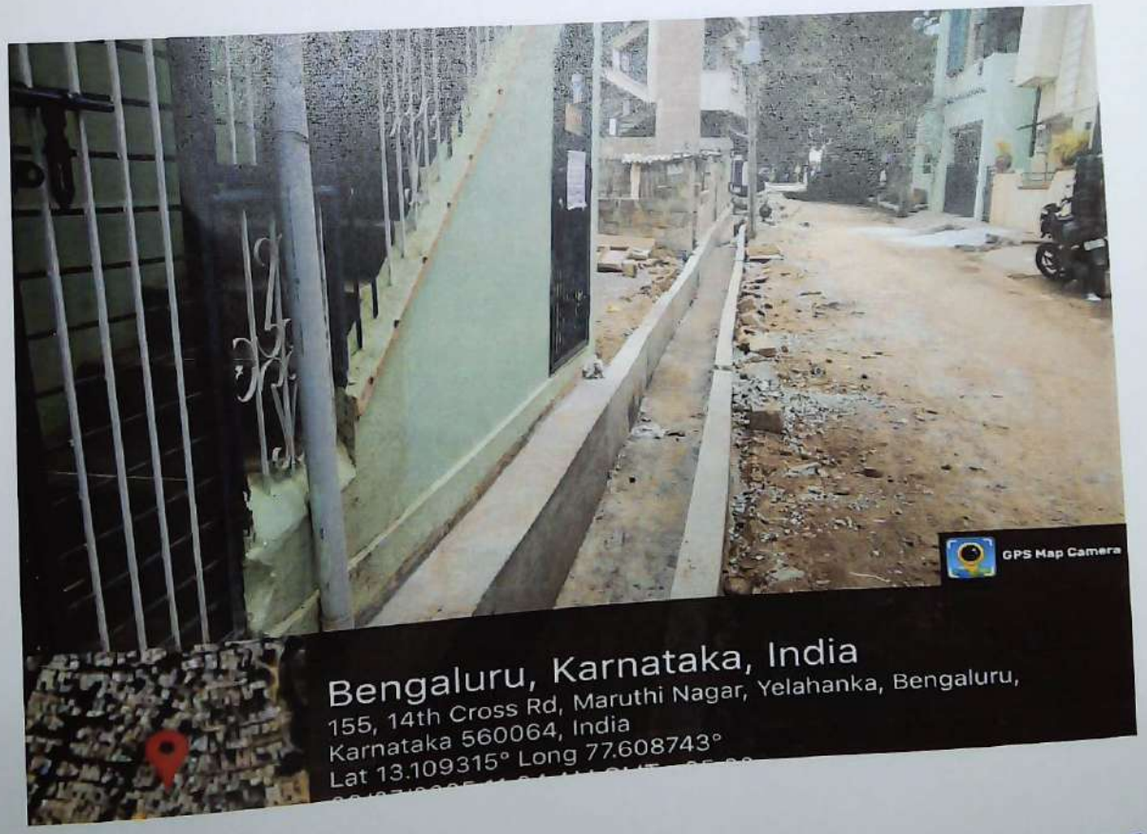
GPS Map Camera
Bengaluru, Karnataka, India
155, 14th Cross Rd, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.109315° Long 77.608743°

A.E

A.E.E

RESURFACING OF ROADS AT MARUTHINAGARA 3rd MAIN 6th, 7th AND 8th CROSS ROADS IN KEMPEGOWDA WARD NO-01

GPS Map Camera
Bengaluru, Karnataka, India
203, 13 Cross Rd, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.109253° Long 77.608534°

GPS Map Camera
Bengaluru, Karnataka, India
118, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.109183° Long 77.60982°

A.E.E.

A.E

RESURFACING OF ROADS AT MARUTHINAGARA 3rd MAIN 6th, 7th AND 8th CROSS ROADS IN KEMPEGOWDA WARD NO-01

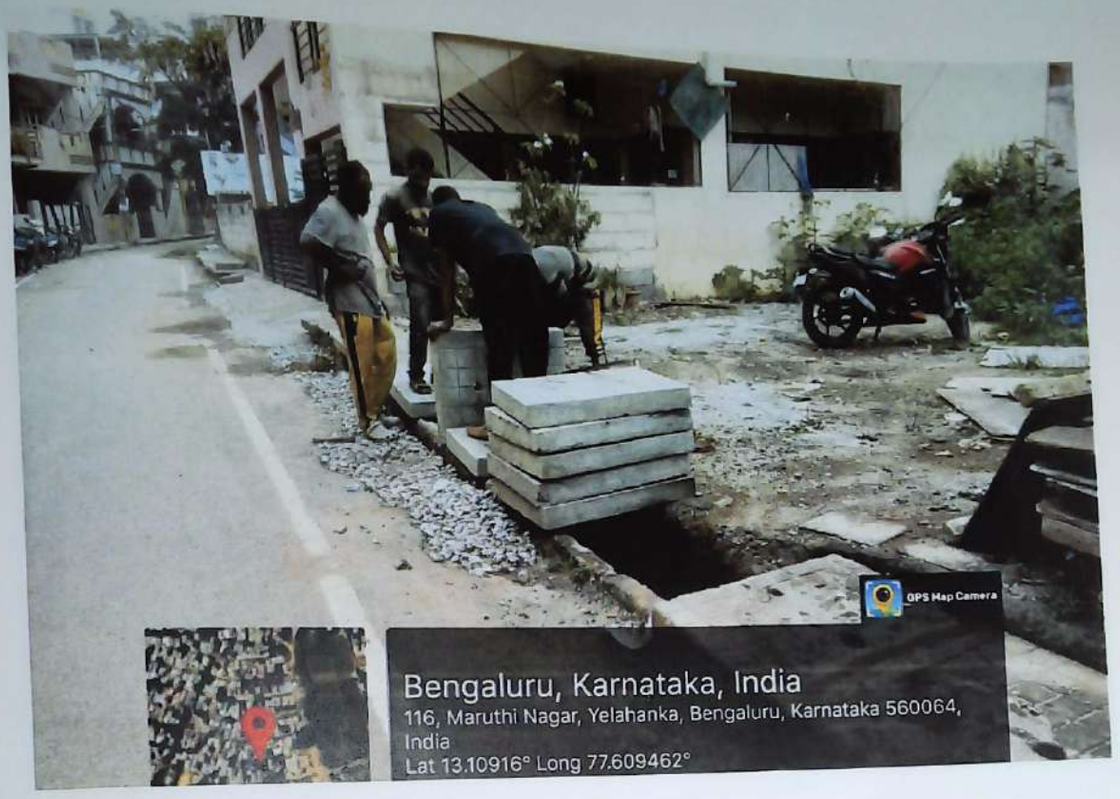
GPS Map Camera
Bengaluru, Karnataka, India
116, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.10916° Long 77.609462°

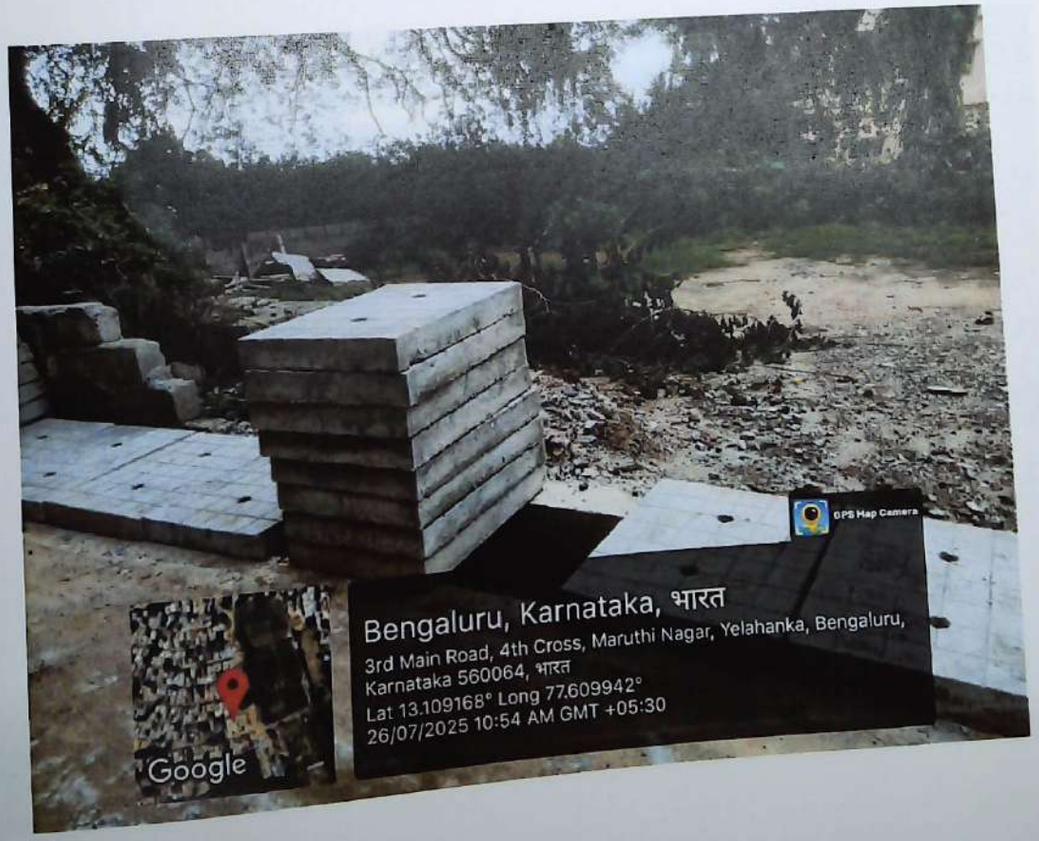
GPS Map Camera
Bengaluru, Karnataka, भारत
3rd Main Road, 4th Cross, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, भारत
Lat 13.109168° Long 77.609942°
26/07/2025 10:54 AM GMT +05:30
Google

A.E

A.E.E.

A.E.E

RESURFACING OF ROADS AT MARUTHINAGARA 3rd MAIN 6th, 7th AND 8th CROSS ROADS IN KEMPEGOWDA WARD NO-01

GPS Map Camera
Bengaluru, Karnataka, India
207, Palanahalli, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.109235° Long 77.608709°

GPS Map Camera
Bengaluru, Karnataka, India
3rd Main Road, 4th Cross, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.109161° Long 77.609961°

A.E.E.

A.E

RESURFACING OF ROADS AT MARUTHINAGARA 3rd MAIN 6th, 7th AND 8th CROSS ROADS IN KEMPEGOWDA WARD NO-01

Bengaluru, Karnataka, India
3rd Main Road, 4th Cross, Maruthi Nagar, Yelahanka,
Bengaluru, Karnataka 560064, India
Lat 13.109162° Long 77.609798°

Bengaluru, Karnataka, India
207, Patanahalli, Maruthi Nagar, Yelahanka, Bengaluru,
Karnataka 560064, India
Lat 13.109138° Long 77.608679°

A.E.E.

A.E

A.E

RESURFACING OF ROADS AT MARUTHINAGARA 3rd MAIN 6th, 7th AND 8th CROSS ROADS IN KEMPEGOWDA WARD NO-01

GPS Map Camera
Bengaluru, Karnataka, India
3rd Main Road, 4th Cross, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.109125° Long 77.609875°

GPS Map Camera
Bengaluru, Karnataka, India
182, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.109173° Long 77.608788°

A.E

A.E.E.

RESURFACING OF ROADS AT MARUTHINAGARA 3rd MAIN 6th, 7th AND 8th CROSS ROADS IN KEMPEGOWDA WARD NO-01

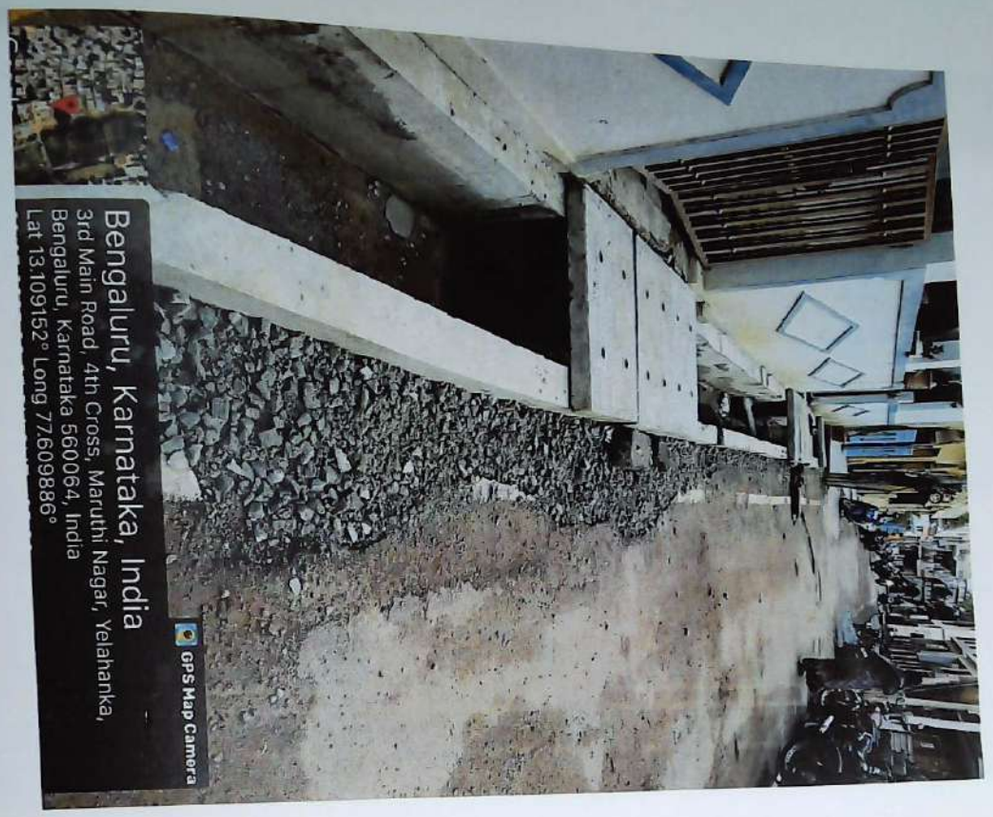
Bengaluru, Karnataka, India
3rd Main Road, 4th Cross, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.109152° Long 77.609886°
GPS Map Camera

GPS Map Camera
Bengaluru, Karnataka, India
259, 6th Cross Rd, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560001, India
Lat 13.108921° Long 77.608679°
25/07/2025 12:35 PM GMT +05:30
Google

A.E.E.

A.E

RESURFACING OF ROADS AT MARUTHINAGARA 3rd MAIN 6th, 7th AND 8th CROSS ROADS IN KEMPEGOWDA WARD NO-01

GPS Map Camera
Bengaluru, Karnataka, India
118, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.109186° Long 77.609676°

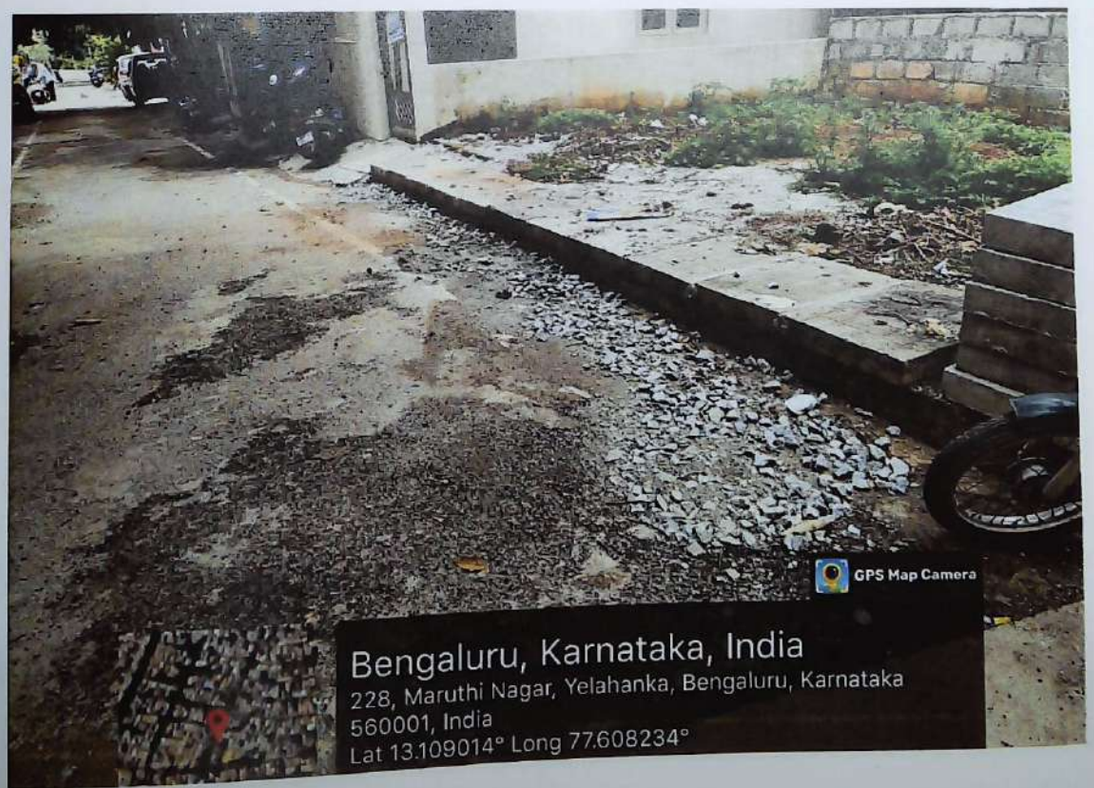
GPS Map Camera
Bengaluru, Karnataka, India
228, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560001, India
Lat 13.109014° Long 77.608234°

A.E

A.E.E

RESURFACING OF ROADS AT MARUTHINAGARA 3rd MAIN 6th, 7th AND 8th CROSS ROADS IN KEMPEGOWDA WARD NO-01

GPS Map Camera
Bengaluru, Karnataka, India
259, 6th Cross Rd, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560001, India
Lat 13.108921° Long 77.608679°

GPS Map Camera
Bengaluru, Karnataka, India
115, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.109147° Long 77.609419°

A.E

A.E.E.

RESURFACING OF ROADS AT MARUTHINAGARA 3rd MAIN 6th, 7th AND 8th CROSS ROADS IN KEMPEGOWDA WARD NO-01

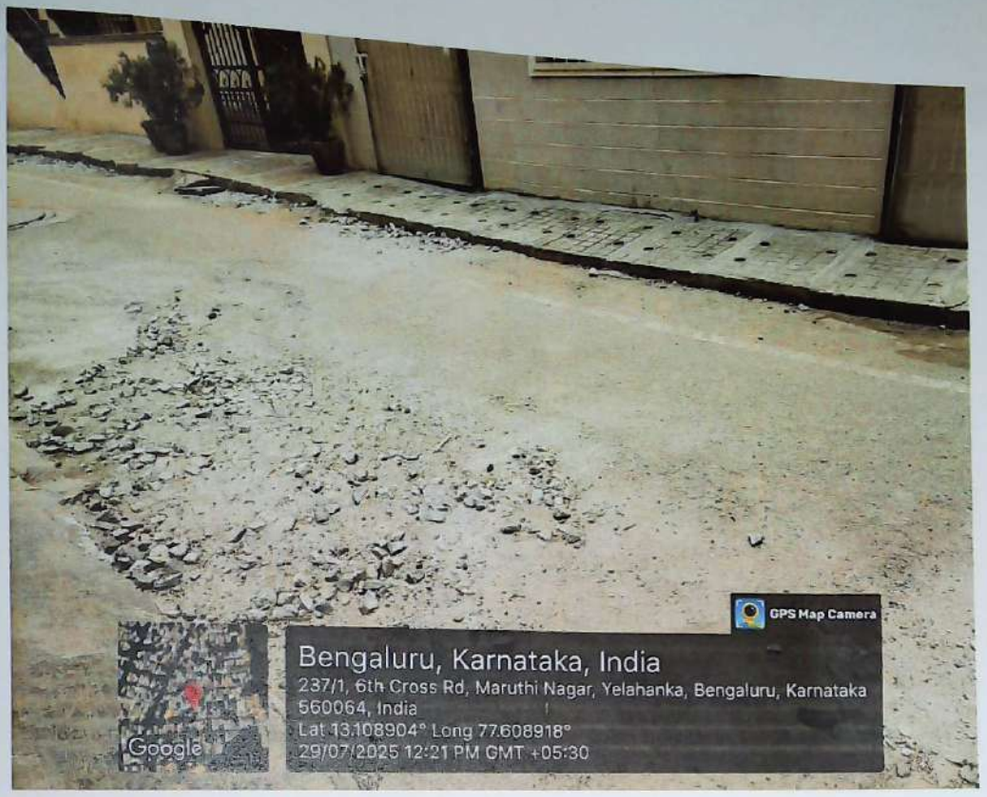
GPS Map Camera
Bengaluru, Karnataka, India
237/1, 6th Cross Rd, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.108904° Long 77.608918°
29/07/2025 12:21 PM GMT +05:30
Google

GPS Map Camera
Bengaluru, Karnataka, India
Shahana Manzil, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.109511° Long 77.610007°

A.E

A.E.E.

RESURFACING OF ROADS AT MARUTHINAGARA 3rd MAIN 6th, 7th AND 8th CROSS ROADS IN KEMPEGOWDA WARD NO-01

GPS Map Camera
Bengaluru, Karnataka, India
26/2, 2nd Main Rd, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.106504° Long 77.608286°

GPS Map Camera
Bengaluru, Karnataka, India
26/2, 2nd Main Rd, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.106446° Long 77.608158°

A.E

A.E.E.

RESURFACING OF ROADS AT MARUTHINAGARA 3rd MAIN 6th, 7th AND 8th CROSS ROADS IN KEMPEGOWDA WARD NO-01

GPS Map Camera
Bengaluru, Karnataka, India
106 3rd Main Road, 6th Cross, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.108935° Long 77.61006°

GPS Map Camera
Bengaluru, Karnataka, India
166, 14th Cross Rd, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.109388° Long 77.609598°

A.E.E.

A.E

RESURFACING OF ROADS AT MARUTHINAGARA 3rd MAIN 6th, 7th AND 8th CROSS ROADS IN KEMPEGOWDA WARD NO-01

GPS Map Camera
Bengaluru, Karnataka, India
106 3rd Main Road, 6th Cross, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.108942° Long 77.609962°

GPS Map Camera
Bengaluru, Karnataka, India
106 3rd Main Road, 6th Cross, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.10895° Long 77.610001°

A.E.E.

A.E

RESURFACING OF ROADS AT MARUTHINAGARA 3rd MAIN 6th, 7th AND 8th CROSS ROADS IN KEMPEGOWDA WARD NO-01

GPS Map Camera
Bengaluru, Karnataka, India
118, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.109242° Long 77.609678°

GPS Map Camera
Bengaluru, Karnataka, India
235, 6th Cross Rd, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560001, India
Lat 13.108924° Long 77.608944°
30/07/2025 10:54 AM GMT +05:30
Google

A.E.E.

A.E

RESURFACING OF ROADS AT MARUTHINAGARA 3rd MAIN 6th, 7th AND 8th CROSS ROADS IN KEMPEGOWDA WARD NO-01

GPS Map Camera
Bengaluru, Karnataka, India
209, Palanahalli, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.109072° Long 77.60887°

GPS Map Camera
Bengaluru, Karnataka, India
118, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.109097° Long 77.609742°

A.E

A.E.E.

RESURFACING OF ROADS AT MARUTHINAGARA 3rd MAIN 6th, 7th AND 8th CROSS ROADS IN KEMPEGOWDA WARD NO-01

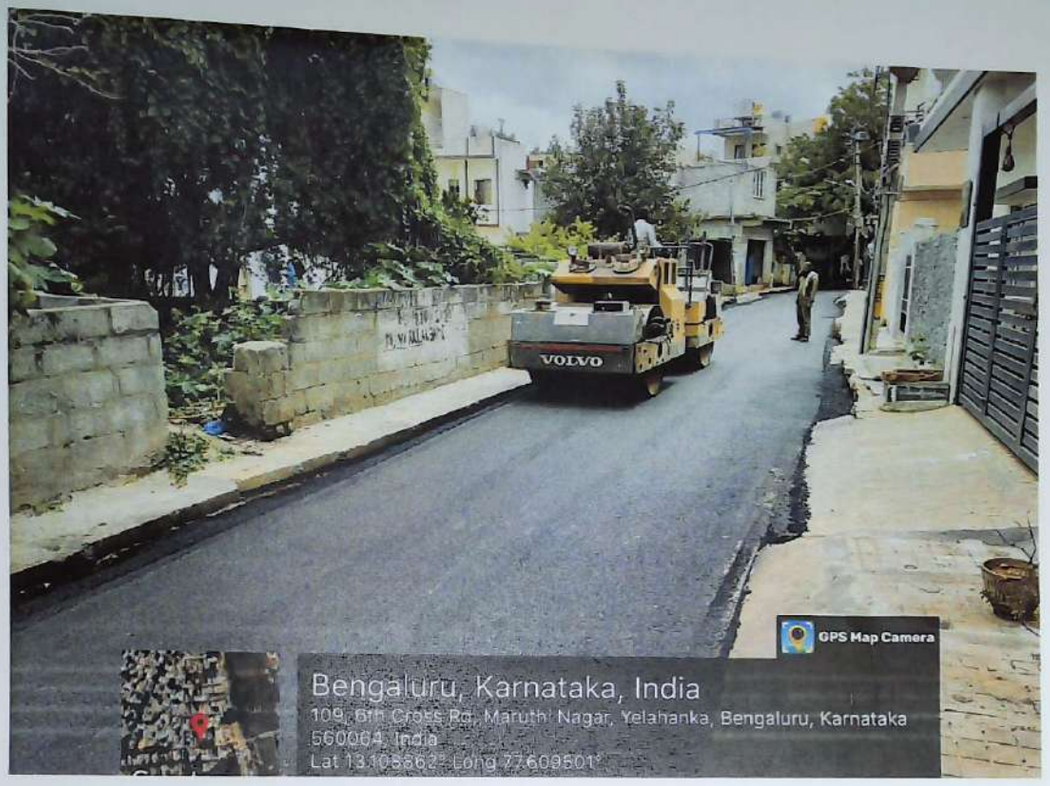
VOLVO
GPS Map Camera
Bengaluru, Karnataka, India
109, 6th Cross Rd, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.109662° Long 77.609501°

Apollo
Apollo
GPS Map Camera
Bengaluru, Karnataka, India
3rd Main Road, 4th Cross, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.109153° Long 77.609941°

A.E

A.E.E.

RESURFACING OF ROADS AT MARUTHINAGARA 3rd MAIN 6th, 7th AND 8th CROSS ROADS IN KEMPEGOWDA WARD NO-01

GPS Map Camera
Bengaluru, Karnataka, India
106 3rd Main Road, 6th Cross, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.108934° Long 77.610135°

GPS Map Camera
Bengaluru, Karnataka, India
Shahana Manzil, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.109509° Long 77.609942°

A.E.E.

A.E

RESURFACING OF ROADS AT MARUTHINAGARA 3rd MAIN 6th, 7th AND 8th CROSS ROADS IN KEMPEGOWDA WARD NO-01

GPS Map Camera
Bengaluru, Karnataka, India
106 3rd Main Road, 6th Cross, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.10895° Long 77.610076°

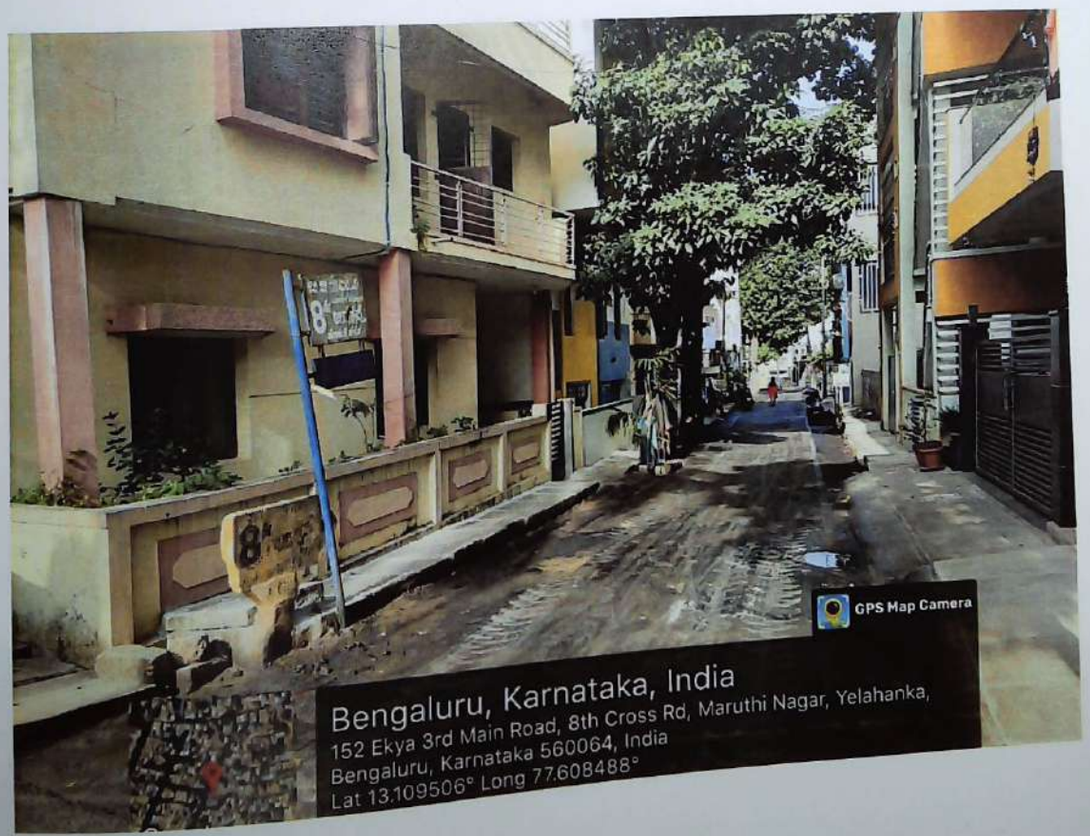
GPS Map Camera
Bengaluru, Karnataka, India
152 Ekya 3rd Main Road, 8th Cross Rd, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.109506° Long 77.608488°

A.E.E

A.E.E.

A.E

RESURFACING OF ROADS AT MARUTHINAGARA 3rd MAIN 6th, 7th AND 8th CROSS ROADS IN KEMPEGOWDA WARD NO-01

GPS Map Camera
Bengaluru, Karnataka, India
152 Ekya 3rd Main Road, 8th Cross Rd, Maruthi Nagar, Yelahanka,
Bengaluru, Karnataka 560064, India
Lat 13.109506° Long 77.6084..°

GPS Map Camera
Bengaluru, Karnataka, India
175/1, Maruthi Nagar 13th Cross Rd, Palahalli, Tirumanahalli,
Bengaluru, Karnataka 560001, India
Lat 13.109253° Long 77.608414°

A.E

A.E.E.

RESURFACING OF ROADS AT MARUTHINAGARA 3rd MAIN 6th, 7th AND 8th CROSS ROADS IN KEMPEGOWDA WARD NO-01

GPS Map Camera
Bengaluru, Karnataka, India
228, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560001, India
Long 77.608259°

GPS Map Camera
Bengaluru, Karnataka, India
214, Maruthi Nagar, Yelahanka, Bengaluru, Karnataka 560064, India
Lat 13.109132° Long 77.60929°

A.E

A.E.E

A.E.E.
